

i21D Front End Loader - W+A1 Spectrum Finishing - Remedial Action
 Contractor: EnviroTrac Environmental Services
 CDM Job No: D-006956 Site No. 1-52-029
 CDM Project Manager: John Blaum

CDM
 100 Crossways Park West
 Woodbury, NY 11797
 Telephone: 516.496.8400
 Fax: 516.496.8864

DAILY REPORT

Day:

S	M	T	W	TH	F	S
---	---	---	---	----	---	---

 Date: 11-Mar-09
 REPORT No. 97
 PAGE No. 1

WEATHER	Clear	Partly Cloudy	Overcast	Rain	Snow
TEMP L/H		44/47			
HUMIDITY	Dry	Moderate	High		
WIND	Calm	Light	Moderate	High	
WIND DIR	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction manager	2x8 hrs	J.Szymanski, M.Rose
EnviroTrac	Operator	1x8hrs	J.Byrnes
EnviroTrac	Technician	2x8 hrs	R.Gimbel, K.Davies
AARCO	Operator	2x8 hrs	A.Sanchez, M.Bonislowski
AARCO	Laborer	2x8 hrs	M.Mazur, J.Torres

EQUIPMENT AT THE SITE I = Idle W = Working

Daewoo 450 skidder - W	AARCO Guzzler Vac Truck - W
Case 590 Backhoe - W	AARCO Support Truck - W
Case 621D Front End Loader - I	CAT 301.5 mini-excavator - W
20' Storage Container - W	
Genie 7-45/25J man lift - W	

HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
All workers onsite were in level D-PPE		

CONSTRUCTION ACTIVITIES

Site Representative: Frank Robinson - CDM
Health and Safety Site Officer: N/A
DESCRIPTION OF WORK PERFORMED AND OBSERVED
1-Tailgate H&S meeting performed before the start of the work day. 2- Air monitoring (dust and VOC's) was not performed due to light rain/drizzle.
2-The east wall repair of 51 Cabot Street was finished under PCO #4 (\$3,384.07). A Genie man lift was used to repair the holes at the top of the wall.
3- Completed excavating west alleyway between sample locations WA-2 and WA-3 to a depth of 2 feet using a mini-excavator and the vac truck.
4-Starting to excavate the east alley way between sample locations EA-2 and EA-3 to a depth of 2-4 feet using the backhoe and using the skid steer to move the soil to the stockpile area. Found some green soil ~20' west of the gas meter ~3' BG, removed as much as we could. Then started at the east end and working west exposing the gas line by hand and the vac truck.
5-After the skid steer scrapped the slab, started to find green material showing through, see photo.

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson Project Manager: John Blaum

PHOTOGRAPHIC LOG

Date: 03/11/09

CDM Job No. D-006956

Spectrum Finishing Remedial Action

SITE No. 1-52-029

PHOTO	DATE	TIME	DESCRIPTION
100_0098.jpg	3/11/2009	PM	Excavating east alleyway.
100_0102.jpg	3/11/2009	PM	Green staining on slab opposite gas meter.
100_0103.jpg	3/11/2009	PM	Completed excavation of west alleyway.
100_0104.jpg	3/11/2009	PM	Green soil in east alleyway excavation ~20' west of gas meter.
100_0105.jpg	3/11/2009	PM	Completed repair of east wall of 51 Cabot Street.
100_0106.jpg	3/11/2009	PM	Excavating east end of east alleyway.

PHOTOS 3/11/09



100_0098.jpg - Excavating east alleyway.



100_0102.jpg - Green staining on slab opposite gas meter.



100_0103.jpg - Completed excavation in west alleyway.




100_104.jpg - Green soil in east alleyway, ~20' west of gas meter.



100_105.jpg - Completed repair of east wall of 51 Cabot Street



100_106.jpg - Excavating east end of east alleyway.

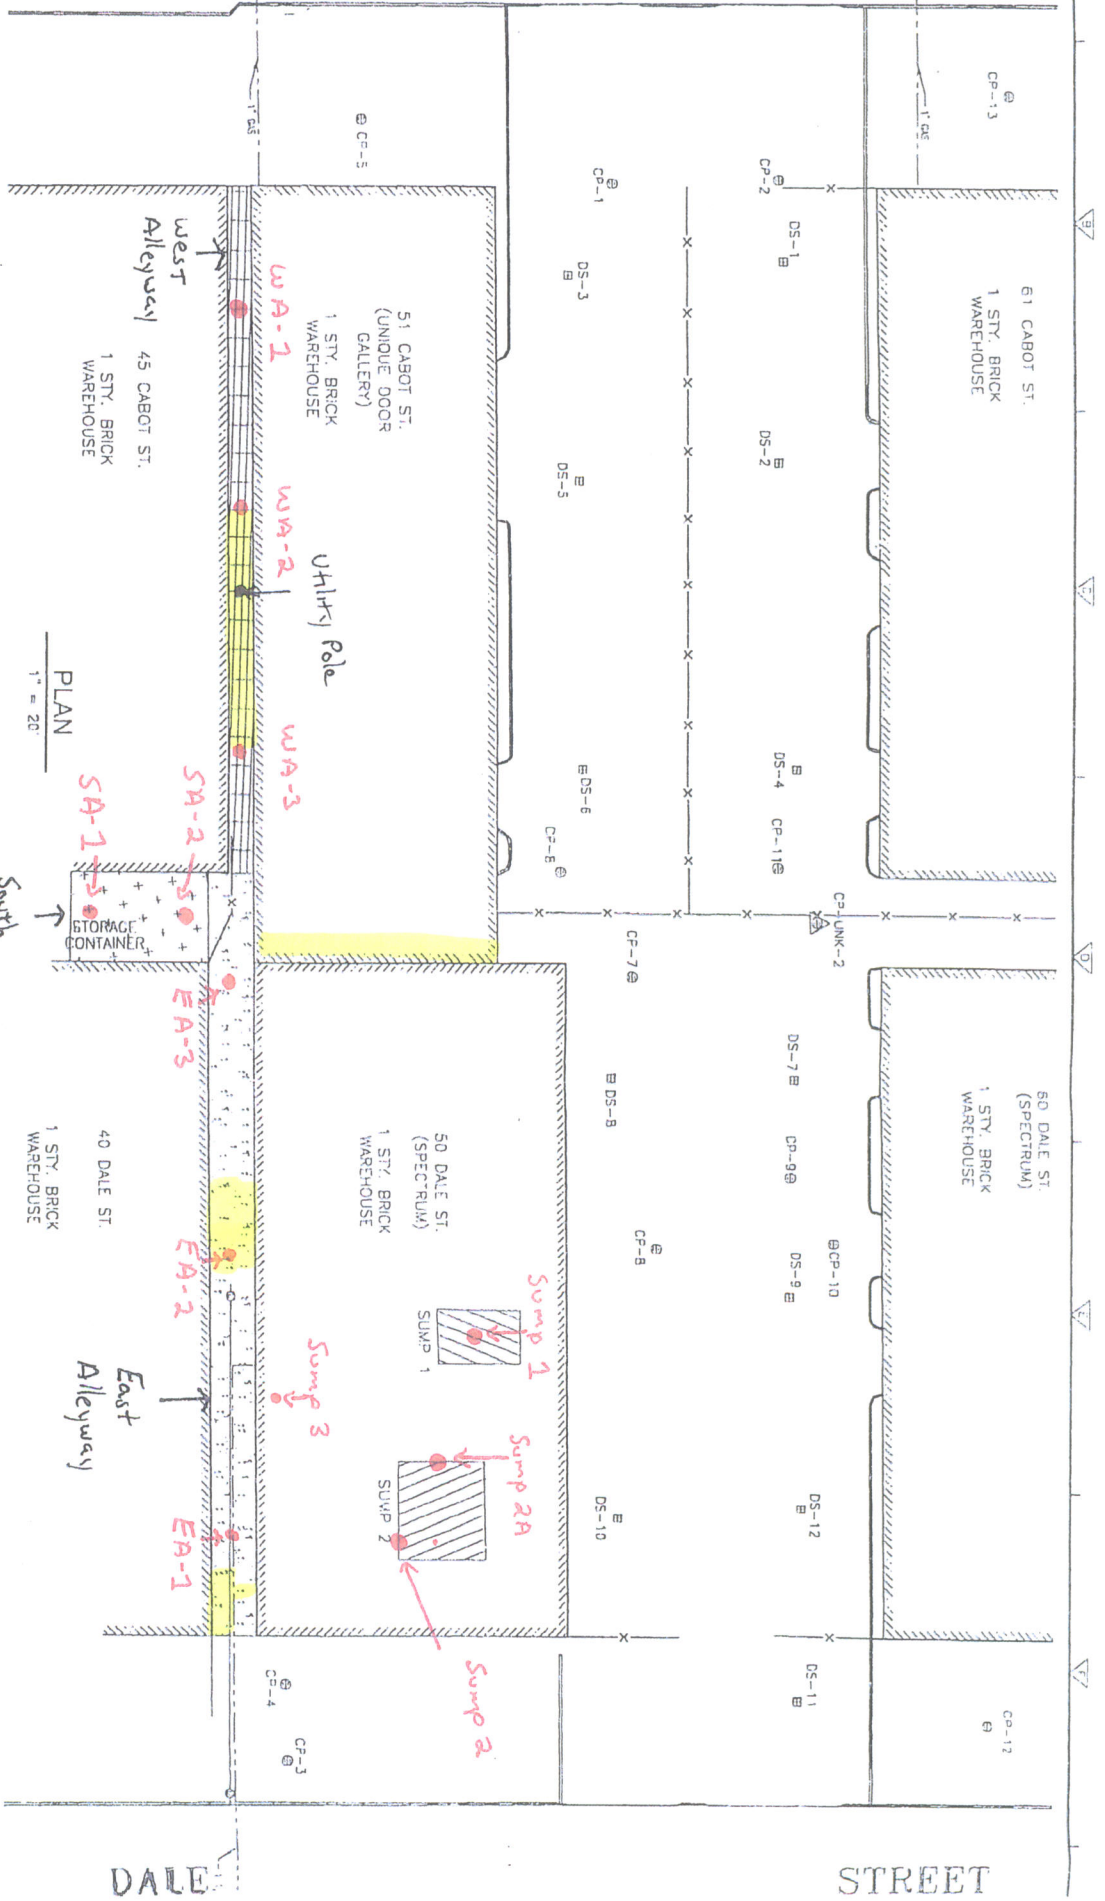

3/11/09
 Work Area

Spectrum Sample Locations
 Note: Sump # 2 was not sampled

EnviroTrac Ltd.
 DEC FIELD REPORT: TIME & MATERIALS REPORT (revised 3/5/09)

DATE: 3/11/09
 WORK DAY: Wednesday
 SITE: Spectrum Finishing

CLIENT: NYSDEC

WORK DESCRIPTION: West/East Alley Excavation

T&M#: ALLO-3/11/09
 FR
 JR

Name	Title	Time Start	Time Arrive Onsite	Time Left Site	Time Finish	Overtime	Total Time
MICHAEL BOULISLAWSKI	Eq Op		7	3			8
JOAN C PRES	laborer						
Andres Sanchez	laborer						
MICHAEL MAZURA	Eq Op						

MATERIALS: RECEIPTS/BILLS ATTACHED
 UNIT COSTS: Reg = Regular Rate Ovr = Overtime Hour

Unit Description	Hourly Rate	Reg Hrs	Ovr. time	Materials/Equipment Description	Daily Rate	Day	Materials/Equipment Description	Day
Equipment Operator	\$74.44	16		Automobiles - Sedans	\$110.00		Guzzler Truck	X
Laborer	\$51.88	16		Light Duty Vehicles (Less Than 1 Ton)	\$130.00		Vactor Truck	
Foreman	\$105.00			Heavy Duty Vehicles (1 Ton or More)	\$150.00		Vactor Jet Truck	
Engineer	\$105.00			Skid Steer	\$320.00		Air Monitoring Equipment	
				Backhoe			Decon Equipment	
				Excavator			Generator Min. 5KW	
				Front End Loader			Air Compressor Min. 200cfm	
				Support Truck		X		
				Mini Excavator		X		

EnviroTrac Ltd.
 DEC FIELD REPORT: TIME & MATERIALS REPORT (revised 3/5/09)

DATE: 2/11/09
 WORK DAY: Wednesday
 CLIENT: NYSDEC

SITE: Spectrum Finishing

T&M#: ET 2/11/09
JKR
Per

WORK DESCRIPTION: East Alley Excavation

Name	Title	Time Start	Time Arrive Onsite	Time Left Site	Time Finish	Overtime	Total Time
Jim Byrnes	Eq Op		9am	1pm			4
Bob Gubel	Eq Op		↓	↓			↓
Ken Davos	Laborer		9am	1pm			4
John Szymski	Foreman		9am	2pm			6
Mike Lege	Engineer						

MATERIALS: RECEIPTS/BILLS ATTACHED
 UNIT COSTS: Reg. Regular Time, Cav. Caving, Hour.

Unit Description	Hourly Rate	Reg Hrs	Ovr time	Materials/Equipment Description	Daily Rate	Day	Materials/Equipment Description	Day
Equipment Operator	\$74.44	8		Automobiles - Sedans	\$110.00	1	Guzzler Truck	
Laborer	\$51.88	4		Light Duty Vehicles (Less Than 1 Ton)	\$130.00	2	Vac Truck	
Foreman	\$105.00	4		Heavy Duty Vehicles (1 Ton or More)	\$150.00	1	Vactor Jet Truck	
Engineer	\$105.00	6		Skid Steer	\$320.00	1	Air Monitoring Equipment	
				Backhoe		1	Decon Equipment	
				Excavator			Generator Min. 5KW	
				Front End Loader		1	Air Compressor Min. 200cfm	
