

Project: Spectrum Finishing - Remedial Action
 Contractor: EnviroTrac Environmental Services
 CDM Job No: D-006956 Site No. 1-52-029
 CDM Project Manager: John Blaum

CDM
 100 Crossways Park West
 Woodbury, NY 11797
 Telephone: 516.496.8400
 Fax: 516.496.8864

DAILY REPORT

Day:

S	M	T	W	TH	F	S
---	---	---	---	----	---	---

 Date: 6-Apr-09
 REPORT No. 115
 PAGE No. 1

WEATHER	Clear	Partly Cloudy	Overcast	Rain	Snow
TEMP L/H		46/56			
HUMIDITY	Dry	Moderate	High		
WIND	Calm	Light	Moderate	High	
WIND DIR	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction Manager	1x8 hrs	M.Rose
EnviroTrac	Operator	2x8 hrs	B.Byrnes, B.Gimbel
EnviroTrac	Technician	2x8 hrs	R.Maletta, K.Davies

EQUIPMENT AT THE SITE

I = Idle W = Working

20" Storage Container - W	
Case CX130 Excavator - W	
Case 621D Front End Loader - W	
Daewoo 450 skidder - W	

HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
All workers onsite were in modified level D-PPE (tyvek and booties)		

CONSTRUCTION ACTIVITIES

Site Representative: Frank Robinson - CDM
Health and Safety Site Officer: N/A
DESCRIPTION OF WORK PERFORMED AND OBSERVED
1-Tailgate H&S meeting performed before the start of the work day. monitoring for dust and VOC's was not performed today due to rain 2-Air
3-While moving material to construct a ramp to get to the contaminated (as per sample results) area around SEB-3 and SES-5, found more green soil/chunks in NE corner near the fire main. Dug down an additional 3' to clean this area out.
4-Excavated material by the area around SEB-3 and SES-5 in the eastern part of the excavation. Could not finish due to having to stop at 0915 due to heavy rain and expected thunder storms.

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson Project Manager: John Blaum

PHOTOGRAPHIC LOG
6-Apr-09
CDM Job No. D-006956
Spectrum Finishing Remedial Action
SITE No. 1-52-029

PHOTO	DATE	TIME	DESCRIPTION
100_00330.jpg	4/6/2009	AM	Excavator excavating SEB-3/SES-5 area. Green chunk from NE corner
100_00331.jpg	4/6/2009	AM	NE corner excavated, found more green soil/chunks
100_00332.jpg	4/6/2009	AM	End of day, excavated area around SEB-3/SES-5

PHOTOS 4/06/09




100_00330.jpg - Excavator excavating SEB-3/SES-5 area.
Green chunk from NE corner.



100_00331.jpg - NE corner excavated, found more green soil/chunks.



100_00332.jpg - End of day, excavated area around SEB-3/SES-5.

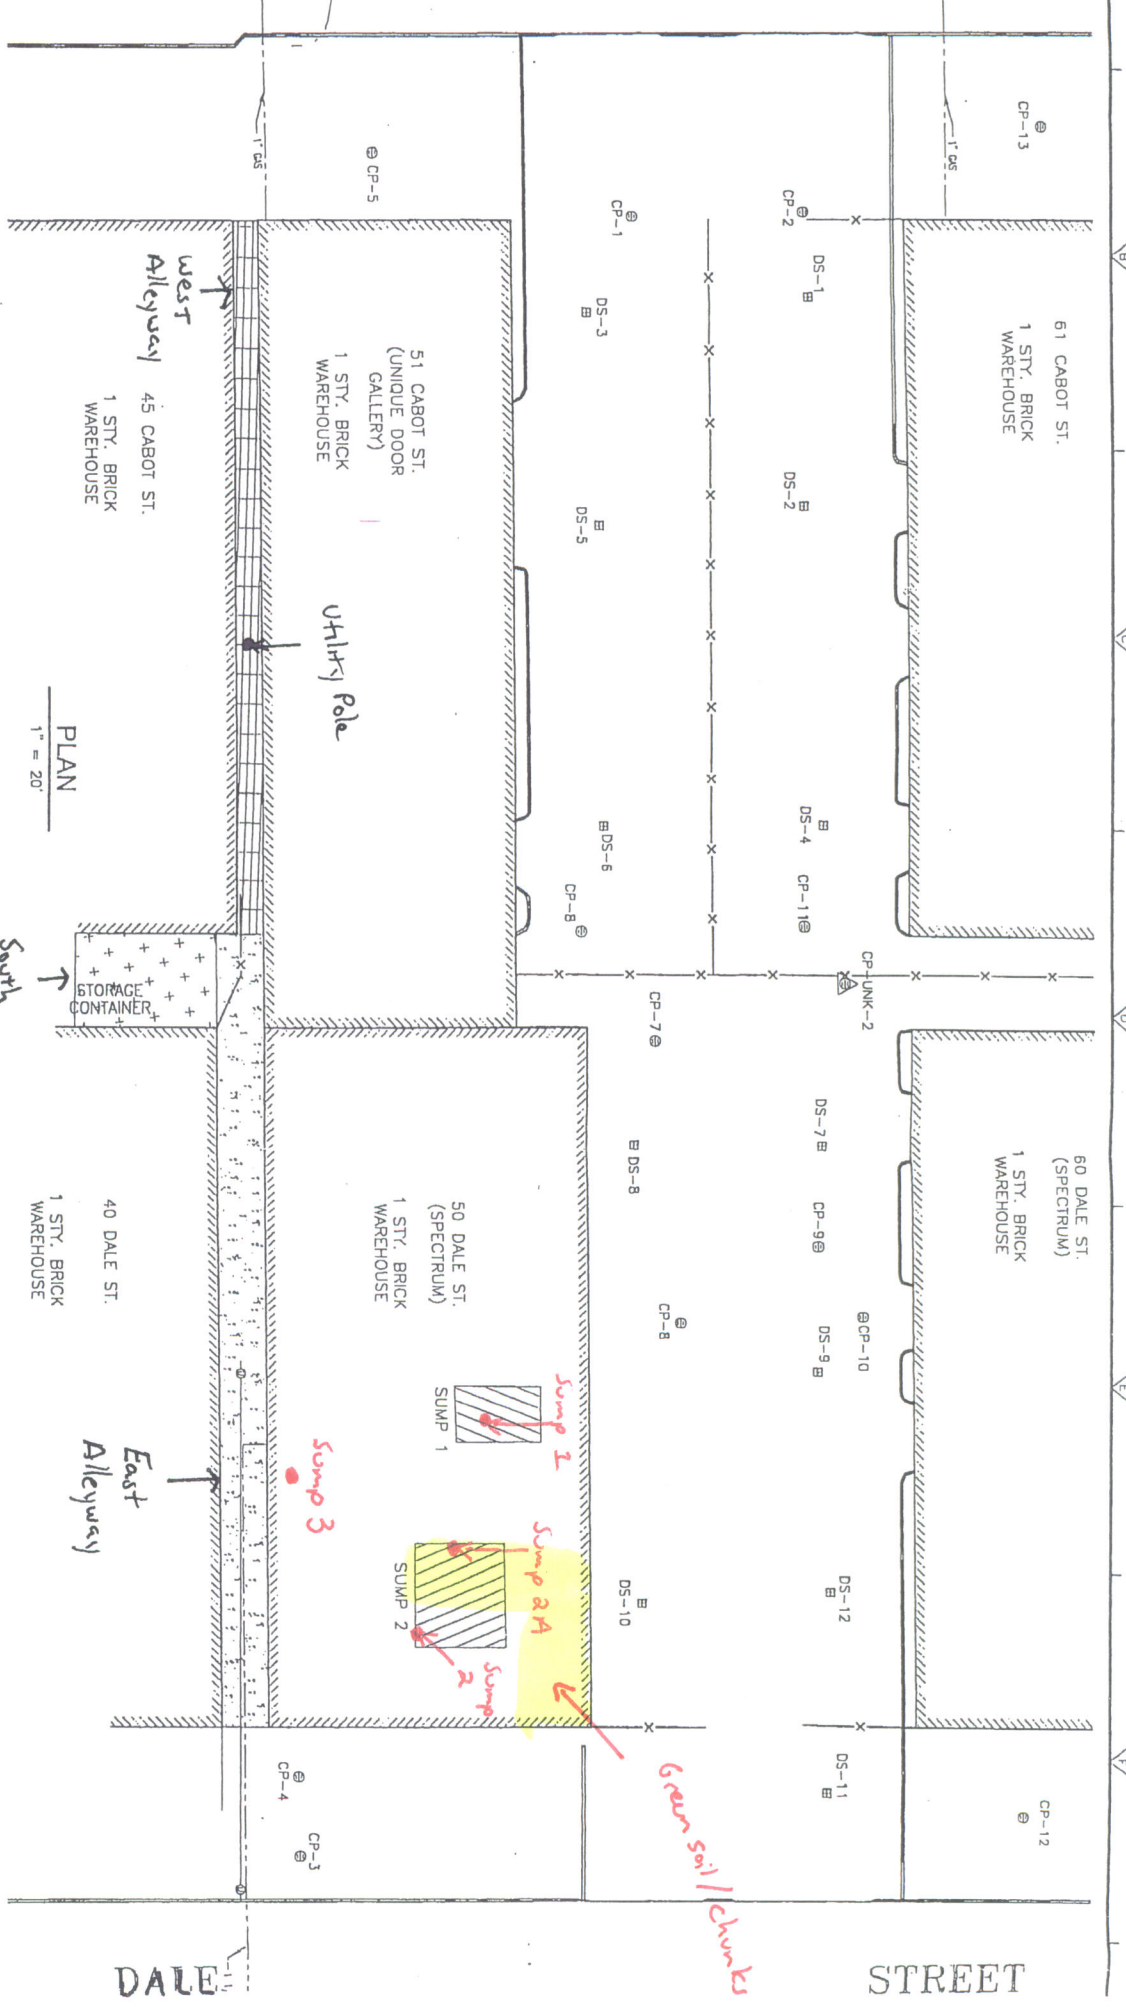


PLAN
1" = 20'

4/6/09
Work Areas

DALE

STREET

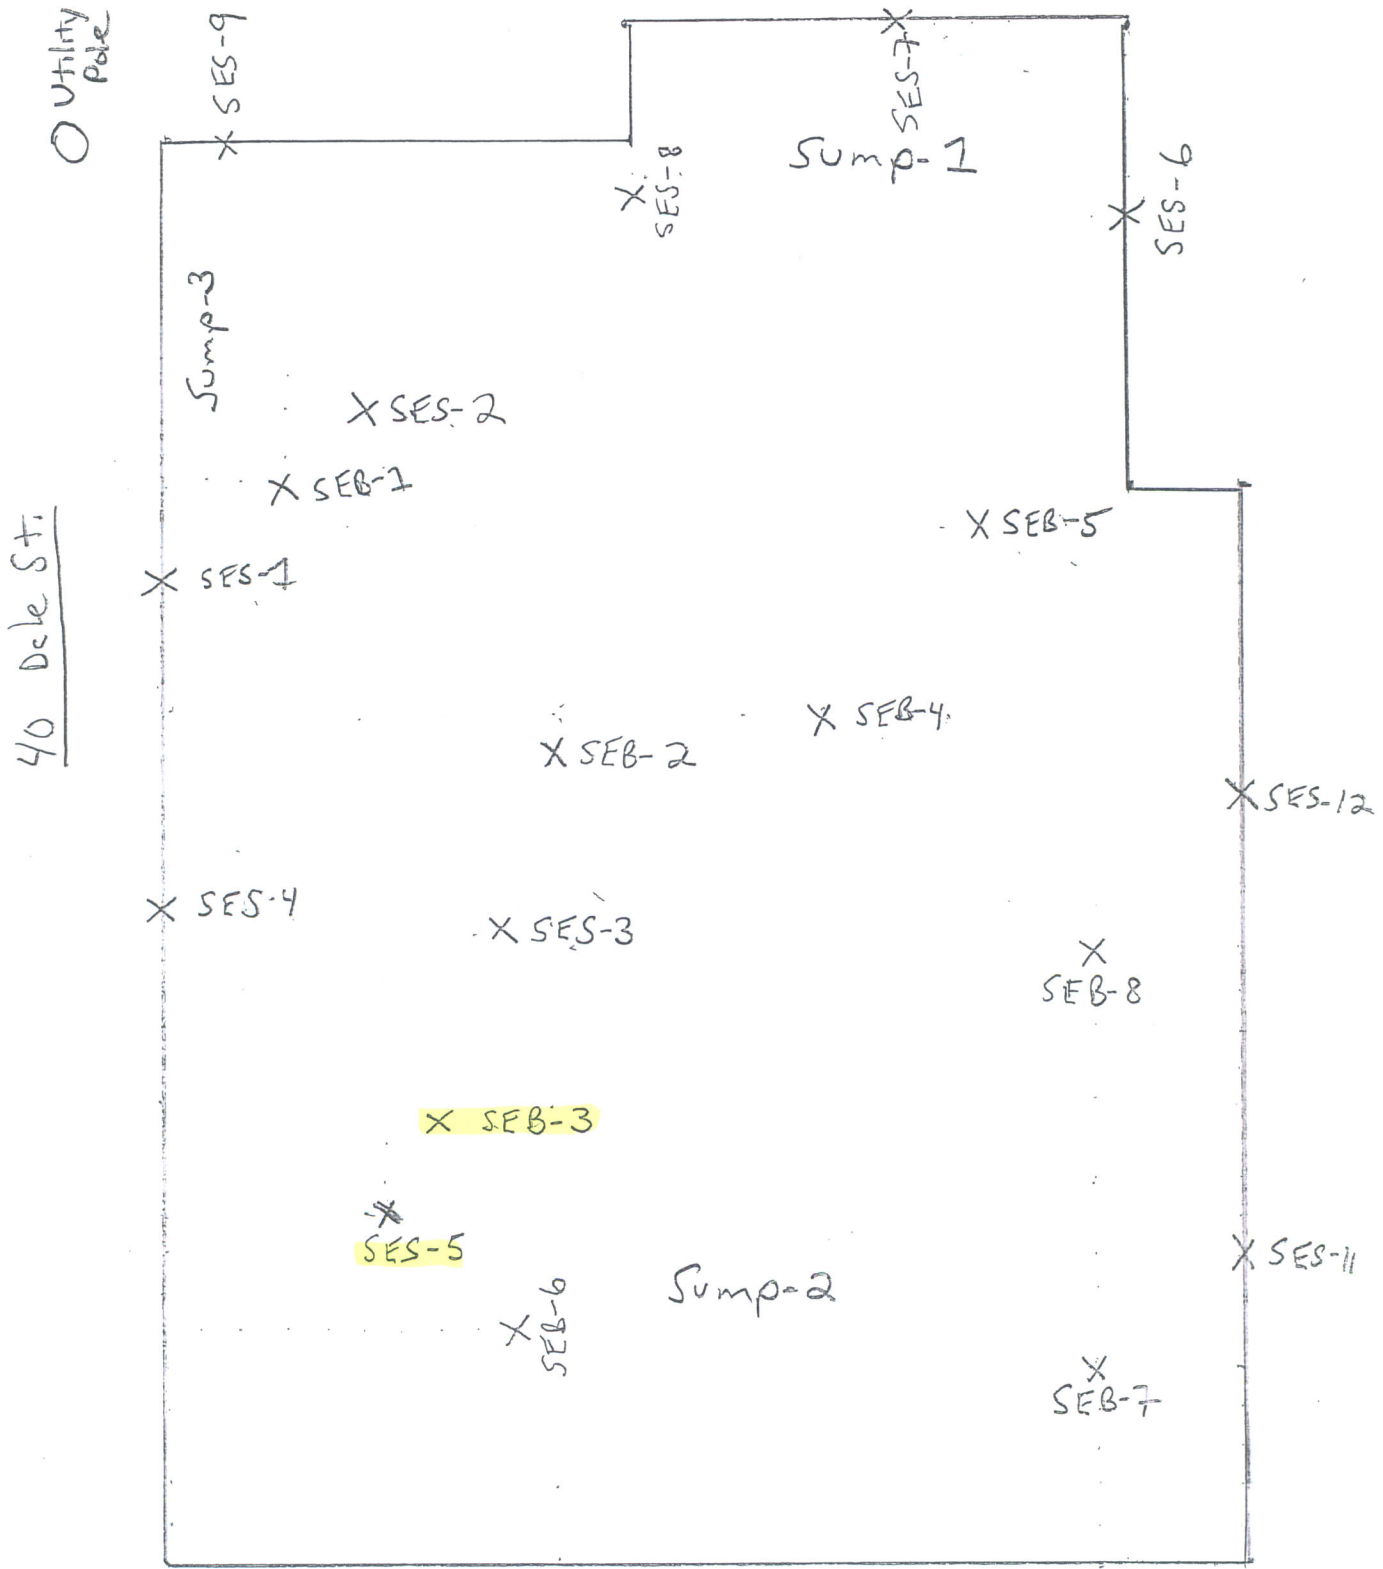

Notes

1 square = 2'
 SES = Sump Excavation Sidewall Sample Location
 SEB = Sump Excavation Bottom Sample Location.

Date St.

X SES-10
