

Project: Spectrum Finishing - Remedial Action  
 Contractor: EnviroTrac Environmental Services  
 CDM Job No: D-006956 Site No. 1-52-029  
 CDM Project Manager: John Blaum

CDM  
 100 Crossways Park West  
 Woodbury, NY 11797  
 Telephone: 516.496.8400  
 Fax: 516.496.8864

### DAILY REPORT

Day: 

S	M	T	W	TH	F	S
---	---	---	---	----	---	---

  
 Date: 17-Jun-09  
 REPORT No. 166  
 PAGE No. 1

<b>WEATHER</b>	Clear	Partly Cloudy	Overcast	Rain	Snow
<b>TEMP L/H</b>		52/65			
<b>HUMIDITY</b>	Dry	Moderate	High		
<b>WIND</b>	Calm	Light	Moderate	High	
<b>WIND DIR</b>	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

#### AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction Manager	1x8 hrs	M.Rose
EnviroTrac	Operator	1x8 hrs	J.Byrnes
EnviroTrac	Technician	1x8 hrs	K.Davies

#### EQUIPMENT AT THE SITE

I = Idle      W = Working

20" Storage Container - W	
Case 621C Front End Loader - I	
CAT 430E Backhoe - I	
CAT 226B skidder - W	

#### HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
		All workers onsite were in level D-PPE

#### CONSTRUCTION ACTIVITIES

<b>Site Representative:</b> Frank Robinson - CDM
<b>Health and Safety Site Officer:</b> N/A
<b>DESCRIPTION OF WORK PERFORMED AND OBSERVED</b>
1- Tailgate H&S meeting performed before the start of the work day.
2-K.P.Edwards Ready Mix delivered 3.5 yd3 of concrete for the replacement sidewalks in front of 51 Cabot St., 40'x4', and 60 Dale St., 10'x4'.
3-Olson Creative Landscaping delivered 40 yd3 of topsoil and 20 yd3 of RCA.
4-EnviroTrac spreading 2-4" of topsoil in front of 51 Cabot St. and 60 Dale St.
5-Janet Greml (SCDHS) on site to inspect UST-5 and 9 and their excavation. Janet did not have any concerns on the tanks or the excavation.

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson      Project Manager: John Blaum

**PHOTOGRAPHIC LOG**

**Date: 06/17/09**

**CDM Job No. D-006956**

**Spectrum Finishing Remedial Action**

**SITE No. 1-52-029**

<b>PHOTO</b>	<b>DATE</b>	<b>TIME</b>	<b>DESCRIPTION</b>
100_0837.jpg	6/17/2009	AM	Pouring concrete for replacement sidewalk in front of 60 Dale St.
100_0838.jpg	6/17/2009	AM	Pouring concrete for replacement sidewalk in front of 61 Cabot St.
100_0839.jpg	6/17/2009	AM	Finished replacement sidewalk in front of 60 Dale St.
100_0840.jpg	6/17/2009	AM	Finished replacement sidewalk in front of 61 Cabot. St.
100_0841.jpg	6/17/2009	PM	Finished applying topsoil (but not seed) to the front of 51 Cabot St.
100_0842.jpg	6/17/2009	PM	Partially applied topsoil (but not seed) to the front of 51 Cabot St.

# PHOTOS 6-17-09



100\_0837.jpg - Pouring concrete for replacement sidewalk in front of 60 Dale St.



100\_0838.jpg - Pouring concrete for replacement sidewalk in front of 61 Cabot St.





**100\_0839.jpg - Finished replacement sidewalk in front of 60 Dale St.**



**100\_0840.jpg - Finished replacement sidewalk in front of 61 Cabot St.**




**100-0841.jpg - Finished applying topsoil (but not seed) to the front of 51 Cabot St.**



**100\_0842.jpg - Partially applied topsoil (but not seed) to the front of 60 Dale St.**



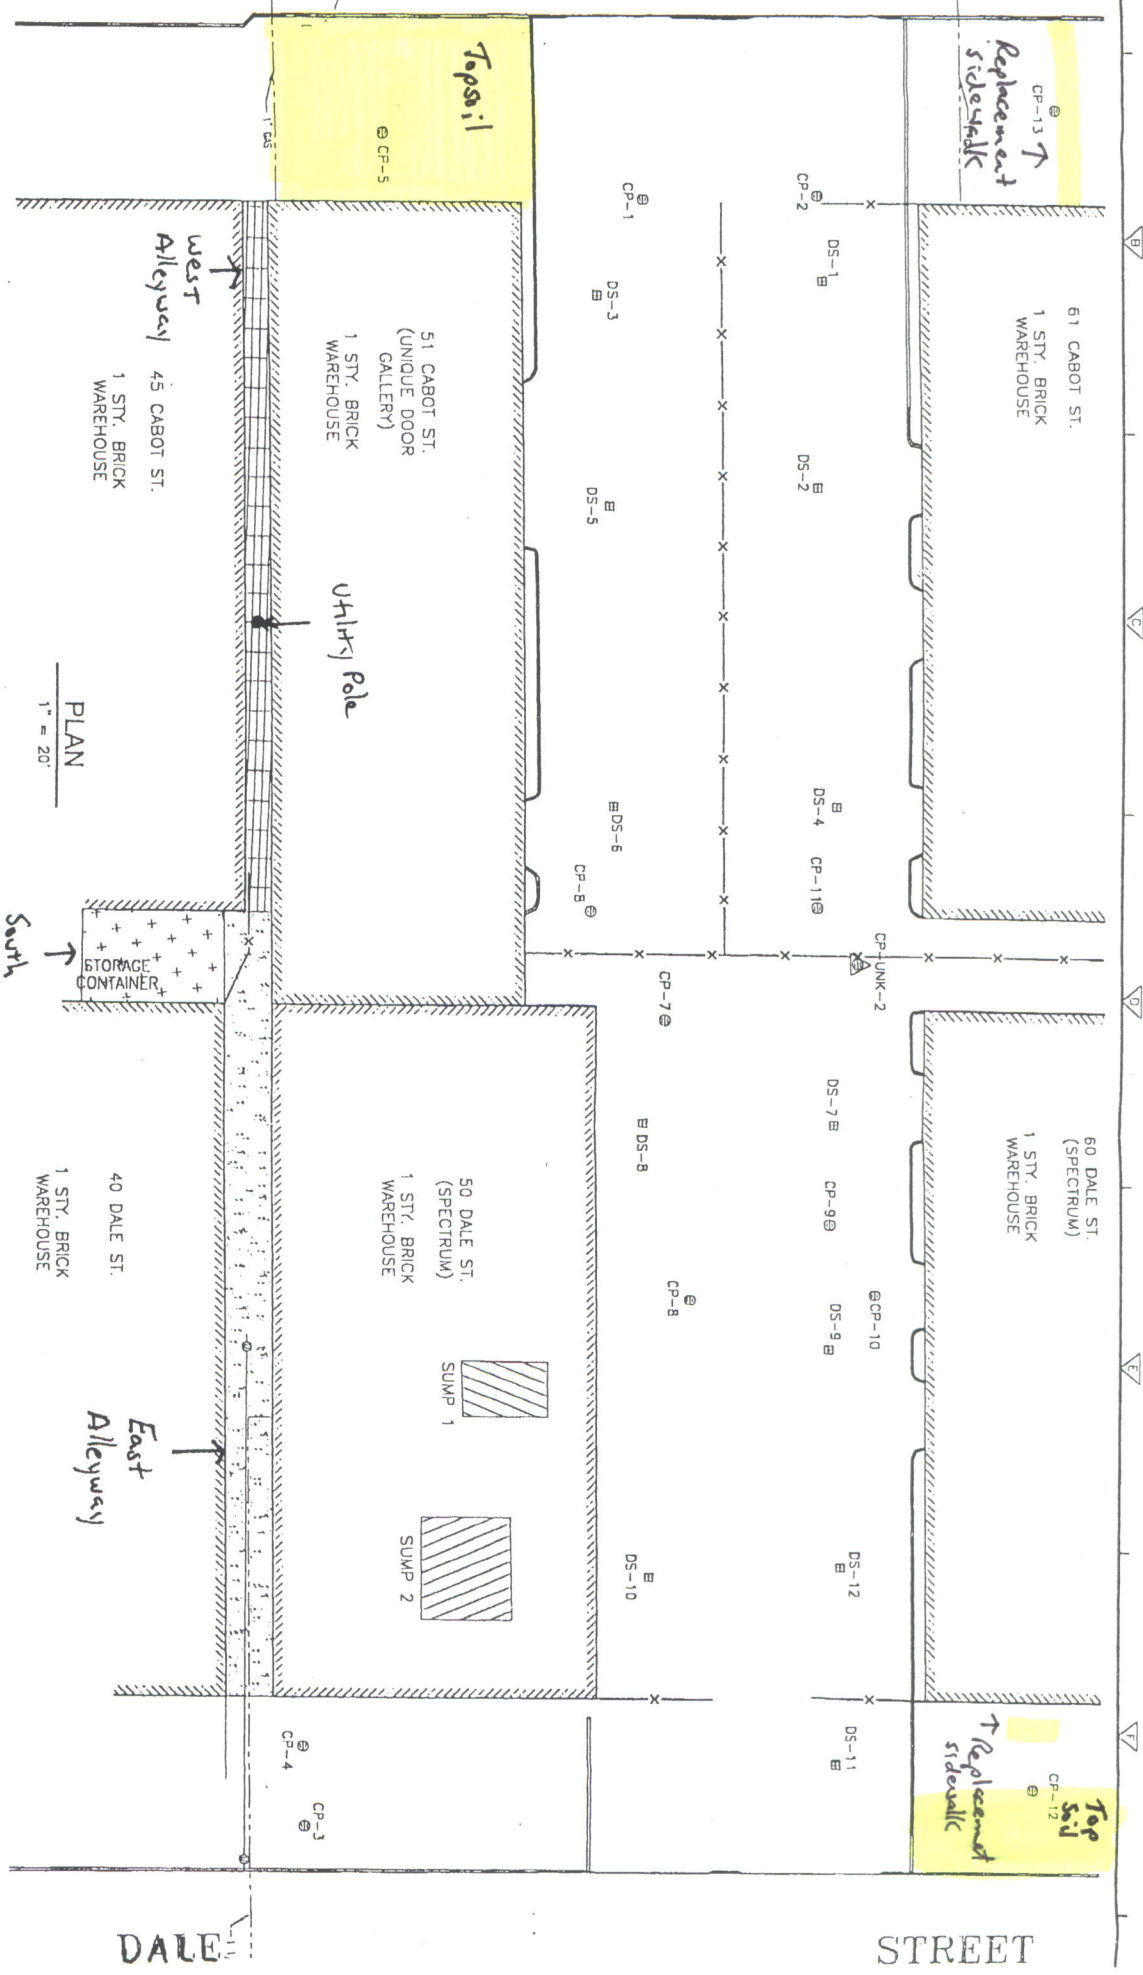

PLAN  
1" = 20'

6/17/69

Work Areas
