

Project: Spectrum Finishing - Remedial Action
 Contractor: EnviroTrac Environmental Services
 CDM Job No: D-006956 Site No. 1-52-029
 CDM Project Manager: John Blaum

CDM
 100 Crossways Park West
 Woodbury, NY 11797
 Telephone: 516.496.8400
 Fax: 516.496.8864

DAILY REPORT

Day:

S	M	T	W	TH	F	S
---	----------	---	---	----	---	---

 Date: 22-Jun-09
 REPORT No. 169
 PAGE No. 1

WEATHER	Clear	Partly Cloudy	Overcast	Rain	Snow
TEMP L/H		66/74			
HUMIDITY	Dry	Moderate	High		
WIND	Calm	Light	Moderate	High	
WIND DIR	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction Manager	1x8 hrs	M.Rose
EnviroTrac	Operator	1x8 hrs	J.Byrnes
EnviroTrac	Technician	2x8 hrs	K.Davies, S. Smith

EQUIPMENT AT THE SITE

I = Idle W = Working

20" Storage Container - W	
Case 621C Front End Loader - I	
CAT 430E Backhoe - I	
CAT 226B skidder - W	

HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
		All workers onsite were in level D-PPE

CONSTRUCTION ACTIVITIES

Site Representative: Frank Robinson - CDM
Health and Safety Site Officer: N/A
DESCRIPTION OF WORK PERFORMED AND OBSERVED
1- Tailgate H&S meeting performed before the start of the work day.
2-EnviroTrac graded the existing soil, installed 2-4" of topsoil then seeded the front of 61 Cabot St. EnviroTrac then seeded in front of 51 Cabot St. and 60 Dale St. and re-installed the sign in front of 51 Cabot St.

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson

Project Manager: John Blaum

PHOTOGRAPHIC LOG

Date: 06/22/09

CDM Job No. D-006956

Spectrum Finishing Remedial Action

SITE No. 1-52-029

PHOTO	DATE	TIME	DESCRIPTION
100_0847.jpg	6/22/2009	AM	Spreading topsoil in front of 61 Cabot St.
100_0850.jpg	6/22/2009	AM	Finished site restoration in front of 51 Cabot St.
100_0851.jpg	6/22/2009	AM	Finished site restoration in front of 61 Cabot St.
100_0852.jpg	6/22/2009	AM	Finished site restoration in front of 60 Dale St.

PHOTOS 6-22-09



100_0847.jpg - Spreading topsoil in front of 61 Cabot St.




100_0850.jpg - Finished site restoration in front of 51 Cabot St.



100_0851.jpg - Finished site restoration in front of 61 Cabot St.



100_0852.jpg - Finished site restoration in front of 60 Dale St.

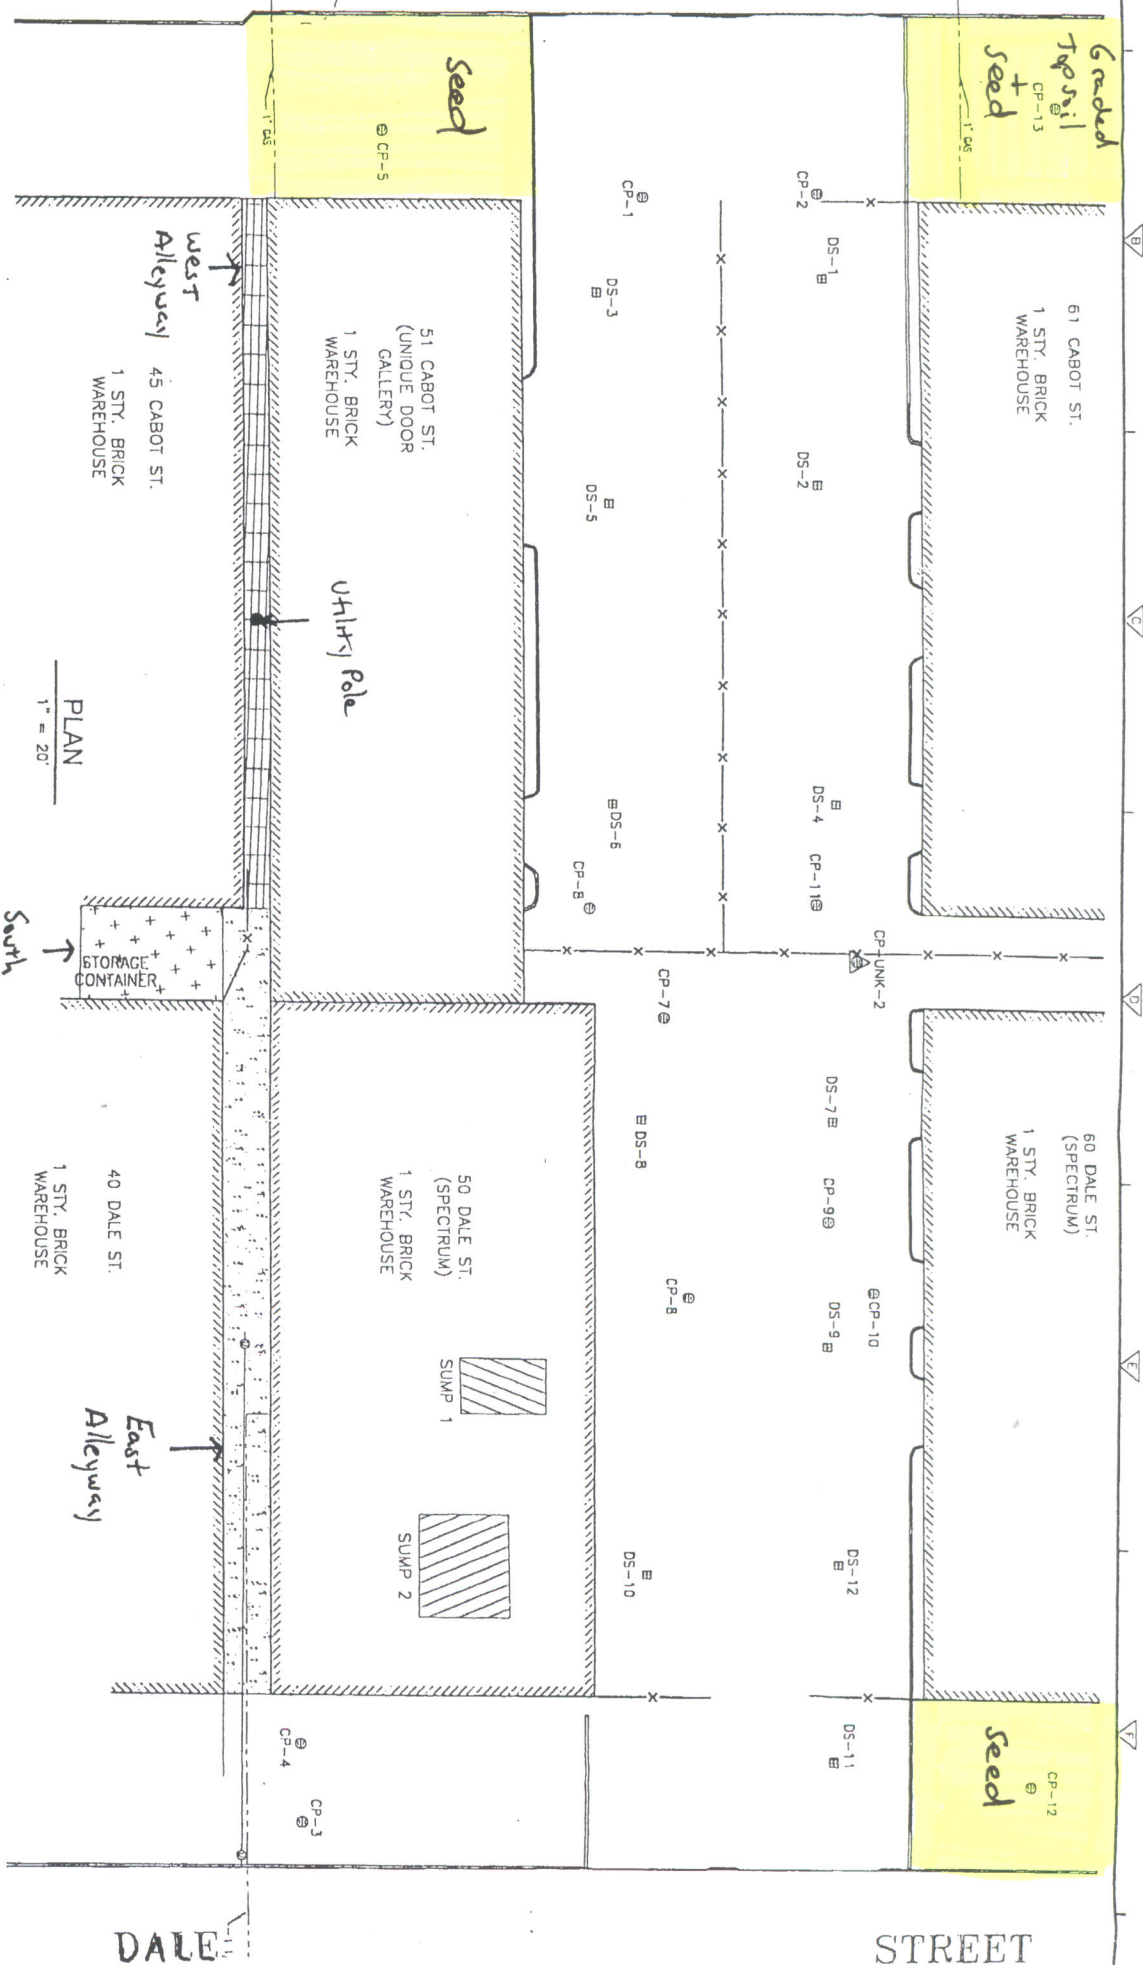

PLAN
1" = 20'

West Alleyway
South Alleyway

East Alleyway

6/22/09

Work Areas

DALE

STREET
