

Project: Spectrum Finishing - Remedial Action
 Contractor: EnviroTrac Environmental Services
 CDM Job No: D-006956 Site No. 1-52-029
 CDM Project Manager: John Blaum

CDM
 100 Crossways Park West
 Woodbury, NY 11797
 Telephone: 516.496.8400
 Fax: 516.496.8864

DAILY REPORT

Day:

S	M	T	W	TH	F	S
---	---	----------	---	----	---	---

 Date: 7-Jul-09
 REPORT No. 179
 PAGE No. 1

WEATHER	Clear	Partly Cloudy	Overcast	Rain	Snow
TEMP L/H		67/81			
HUMIDITY	Dry	Moderate	High		
WIND	Calm	Light	Moderate	High	
WIND DIR	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction manager	1x8 hrs	M.Rose
Accurate Blacktop	Operator	2x8 hrs	D.Flores, T.Saladino
Accurate Blacktop	Laborer	4x8 hrs	R.Nolasco, M.Scioli, R.Tomanor, J.Castro
Accurate Blacktop	Laborer	3x8 hrs	R.Alunto, J.Oelastras, T.Hawe

EQUIPMENT AT THE SITE I = Idle W = Working

20" Storage Container - I	Accurate - Case 570 MXT Loader w/ Grading Box - W
Accurate - Mack Dump truck - W	
Accurate - Case 590 Backhoe - W	
Accurate-Dynapac Roller/Compactor-W	

HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
		All workers onsite were in level D-PPE

CONSTRUCTION ACTIVITIES

Site Representative: Frank Robinson - CDM
Health and Safety Site Officer: N/A
DESCRIPTION OF WORK PERFORMED AND OBSERVED
1- A H&S tailgate meeting was held before the start of work.
2-Accurate Blacktop continued to remove the remnants of the original site asphalt, working from 51 and 61 Cabot St. to the eastern end of the site, 50 and 60 Dale St.
3-Manole covers for the drainage and septic structures were raised as needed to the required elevation.

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson Project Manager: John Blaum

PHOTOGRAPHIC LOG

Date: 07/07/09

CDM Job No. D-006956

Spectrum Finishing Remedial Action

SITE No. 1-52-029

PHOTO	DATE	TIME	DESCRIPTION
100_0933.jpg	7/7/2009	AM	Accurate Blacktop removing asphalt from Cabot and Dale St. areas
100_0935.jpg	7/7/2009	PM	Raised manhole covers at 51 and 61 Cabot St.
100_0936.jpg	7/7/2009	PM	Accurate Blacktop removing asphalt from 60 Dale St.

PHOTOS 7-07-09



100_0926.jpg - Accurate Blacktop removing asphalt Cabot and Dale St. areas



100_0927.jpg - Raised manhole covers at 51 and 61 Cabot St.



100_0928.jpg - Accurate Blacktop removing asphalt from 60 Dale St.

B C D E F

STREET

DALE


61 CABOT ST.
1 STY. BRICK WAREHOUSE

- Removing Asphalt
- Re-grading
- Raising manhole covers

60 DALE ST.
(SPECTRUM)
1 STY. BRICK WAREHOUSE

CP-12



CP-13

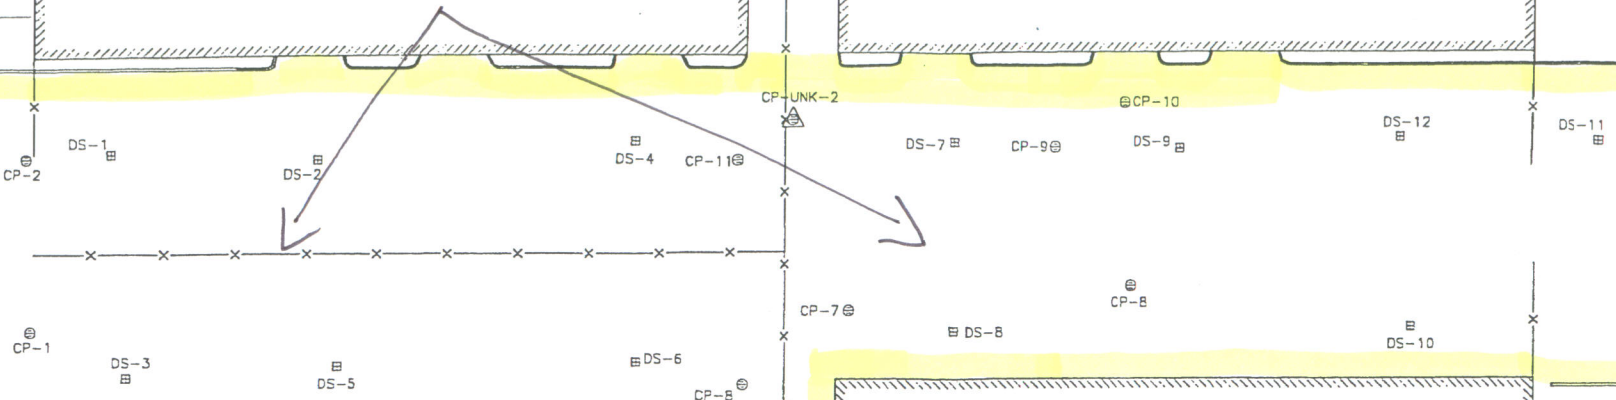

51 CABOT ST.
(UNIQUE DOOR GALLERY)
1 STY. BRICK WAREHOUSE

Utility Pole

50 DALE ST.
(SPECTRUM)
1 STY. BRICK WAREHOUSE



SUMP 1

SUMP 2

West Alleyway

45 CABOT ST.
1 STY. BRICK WAREHOUSE



South Alleyway

East Alleyway

40 DALE ST.
1 STY. BRICK WAREHOUSE

PLAN
1" = 20'

7/7/09

Work Area
