

Project: Spectrum Finishing - Remedial Action
 Contractor: EnviroTrac Environmental Services
 CDM Job No: D-006956 Site No. 1-52-029
 CDM Project Manager: John Blaum

CDM
 100 Crossways Park West
 Woodbury, NY 11797
 Telephone: 516.496.8400
 Fax: 516.496.8864

DAILY REPORT

Day:

S	M	T	W	TH	F	S
---	---	---	---	----	---	---

 Date: 9-Jul-09
 REPORT No. 181
 PAGE No. 1

WEATHER	Clear	Partly Cloudy	Overcast	Rain	Snow
TEMP L/H		62/65			
HUMIDITY	Dry	Moderate	High		
WIND	Calm	Light	Moderate	High	
WIND DIR	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction manager	1x8 hrs	M.Rose
Accurate Blacktop	Operator	2x8 hrs	D.Flores, T.Saladino
Accurate Blacktop	Laborer	4x8 hrs	R.Jimenez, J.Castro, T.Lane, J.Velasques

EQUIPMENT AT THE SITE I = Idle W = Working

20" Storage Container - I	Accurate - Case 570 MXT Loader w/ Grading Box - W
Accurate - Mack Dump truck - W	Accurate - Leeboy 8500 Paver - W
Accurate - Case 590 Backhoe - W	Accurate - Hyster C350C Roller/Compactor -W
Accurate-Dynapac Roller/Compactor-W	

HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
All workers onsite were in level D-PPE		

CONSTRUCTION ACTIVITIES

Site Representative: Frank Robinson - CDM
Health and Safety Site Officer: N/A
DESCRIPTION OF WORK PERFORMED AND OBSERVED
1- A H&S tailgate meeting was held before the start of work.
2-Accutate Blacktop re-graded and compacted the east side of the site, 50 and 60 Dale St., with RCA in preparation for paving the 2" asphalt binder course.
3-Accurate Blacktop paved the site, 51 and 61 Cabot St. and 50 and 60 Dale St., with a 2" asphalt binder course.

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson Project Manager: John Blaum

PHOTOGRAPHIC LOG

Date: 07/09/09

CDM Job No. D-006956

Spectrum Finishing Remedial Action

SITE No. 1-52-029

PHOTO	DATE	TIME	DESCRIPTION
100_0942.jpg	7/9/2009	AM	Accurate Blacktop starting to pave the 2" binder course at 61 Cabot St.
100_0943.jpg	7/9/2009	AM	Accurate Blacktop paving the 2" binder course at 51 Cabot St.
100_0944.jpg	7/9/2009	AM	Accurate Blacktop finished paving the 2" binder course at 51 and 61 Cabot St.
100_0945.jpg	7/9/2009	AM	Accurate Blacktop starting to pave the 2" binder course at 60 Dale St.
100_0946.jpg	7/9/2009	PM	Accurate Blacktop finished paving the 2" binder course, looking west
100_0947.jpg	7/9/2009	PM	Accurate Blacktop finished paving the 2" binder course, looking east

PHOTOS 7-09-09



100_0942.jpg - Accurate Blacktop starting to pave the 2' binder course at 61 Cabot St.



100_0943.jpg - Accurate Blacktop paving the 2" binder course at 51 Cabot St.



100_0944.jpg - Accurate Blacktop finished paving the 2" binder course at 51 and 61 Cabot St.




100_0945.jpg - Accurate Blacktop starting to pave the 2" binder course at 60 Dale St.



100_0946.jpg - Accurate Blacktop finished paving the 2" course, looking west



100_0947.jpg - Accurate finished paving the binder course, looking east

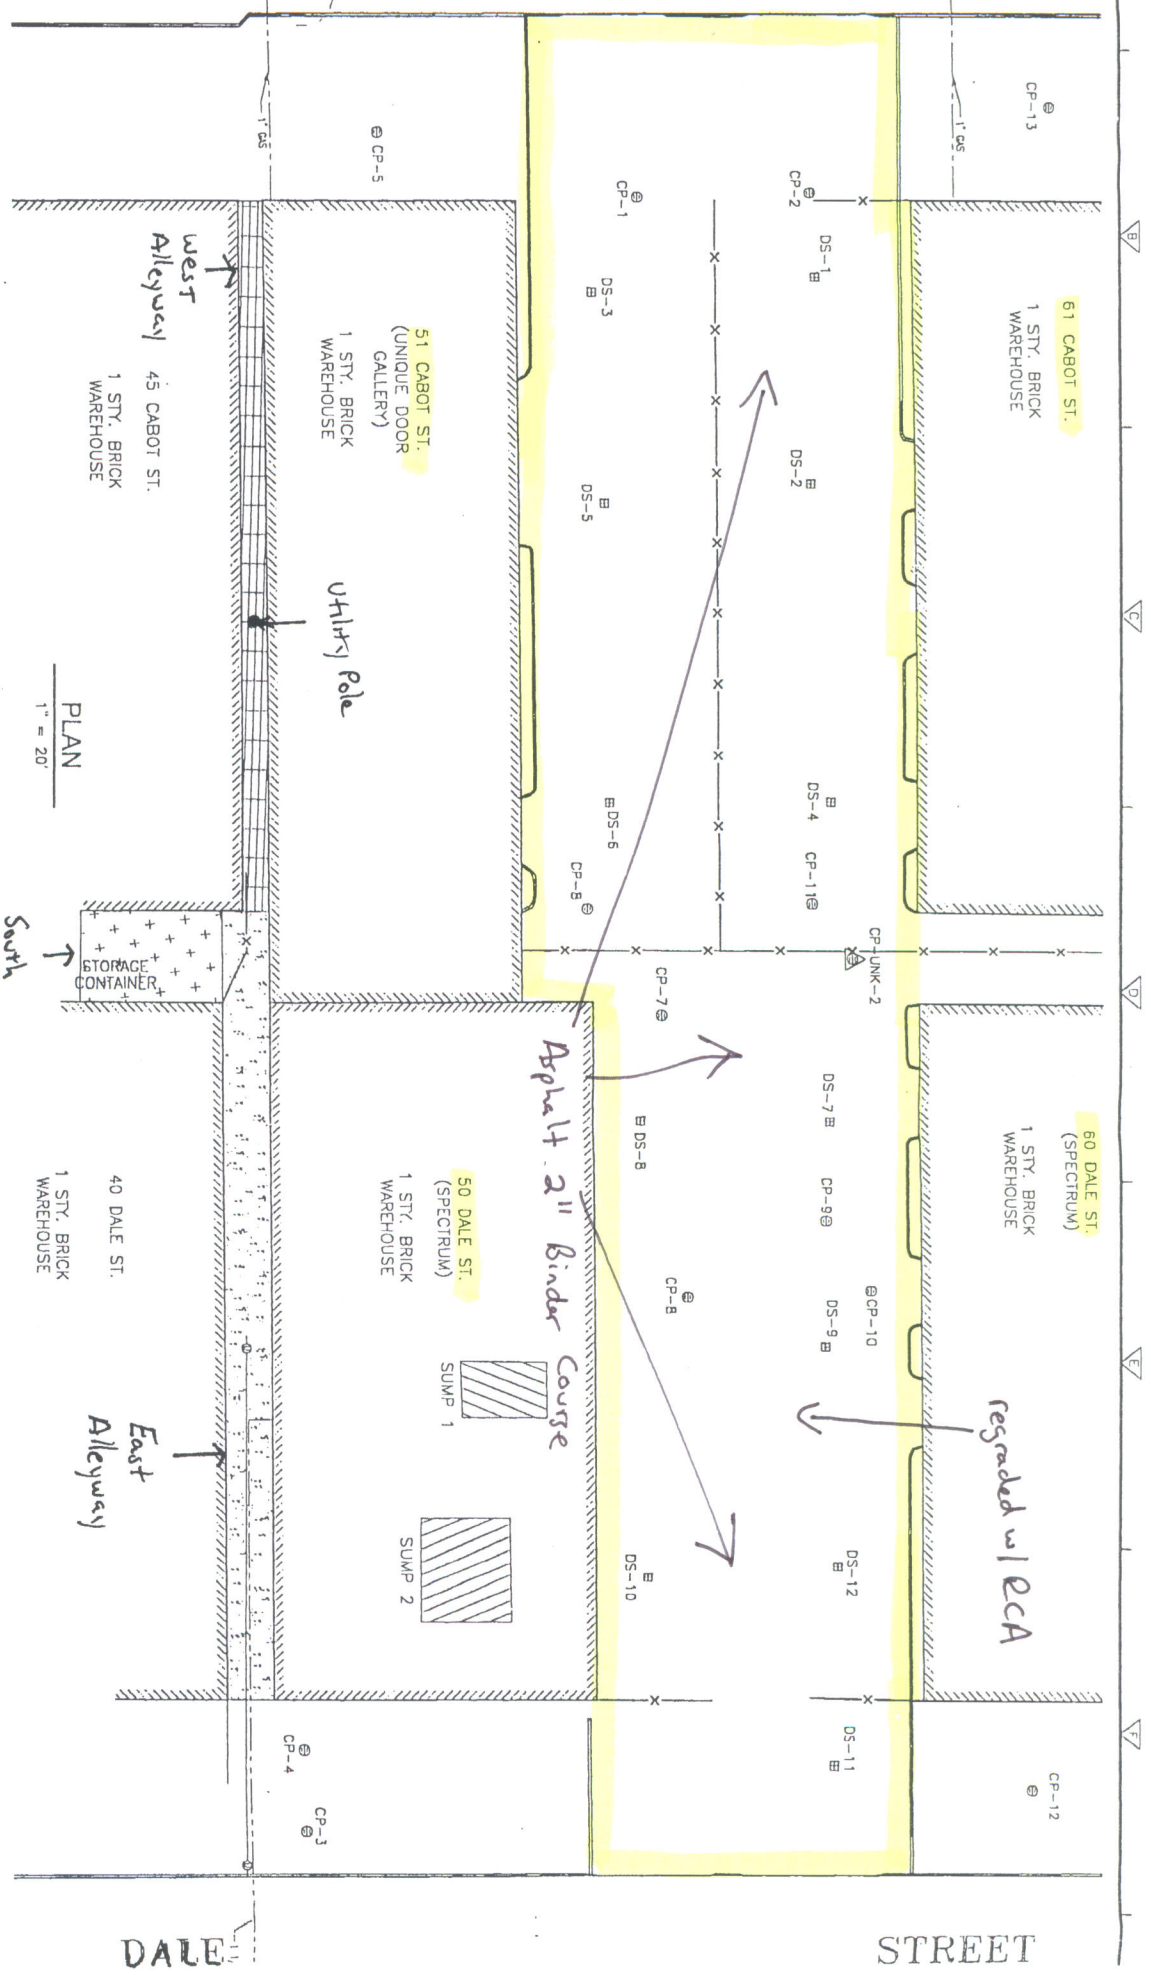

PLAN
1" = 20'

7/9/09
Work Areas

DALE STREET
