

Project: Spectrum Finishing - Remedial Action
 Contractor: EnviroTrac Environmental Services
 CDM Job No: D-006956 Site No. 1-52-029
 CDM Project Manager: John Blaum

CDM
 100 Crossways Park West
 Woodbury, NY 11797
 Telephone: 516.496.8400
 Fax: 516.496.8864

DAILY REPORT

Day:

S	M	T	W	TH	F	S
---	---	---	---	----	---	---

 Date: 13-Jul-09
 REPORT No. 183
 PAGE No. 1

WEATHER	Clear	Partly Cloudy	Overcast	Rain	Snow
TEMP L/H		59/77			
HUMIDITY	Dry	Moderate	High		
WIND	Calm	Light	Moderate	High	
WIND DIR	N	E	S	W	
	NE	SE	SW	NW	

PREPARED BY: F.Robinson TITLE: Inspector

AVERAGE FIELD FORCE

Name of Contractor	Title	Hours Worked	Remarks
EnviroTrac	Construction manager	1x8 hrs	M.Rose
EnviroTrac	Operator	1x8 hrs	J.Byrnes
EnviroTrac	Technician	2x8 hrs	B.Gimbel, K.Davies
Double Eagle Fencing	Supervisor	1x8 hrs	S.Vricciariello
Double Eagle Fencing	Laborer	1x8 hrs	V.Mendoza

EQUIPMENT AT THE SITE I = Idle W = Working

20" Storage Container - W	
Daewoo 450 Skid Steer - W	

HEALTH AND SAFETY

Name	Time (From - To)	Task/Level of PPE
		All workers onsite were in level D-PPE

CONSTRUCTION ACTIVITIES

Site Representative: Frank Robinson - CDM
Health and Safety Site Officer: N/A
DESCRIPTION OF WORK PERFORMED AND OBSERVED
1- A H&S tailgate meeting was held before the start of work.
2-Double Eagle Fencing starting to install replacement fencing by 51/61 Cabot St and 50/60 Dale St. The gates were re-installed at 51/61 Cabot St and 50/60 Dale St. and new post were installed for the fence fabric (see drawing). Top fence rail was installed in the fence by 51 and 61 Cabot St.
3-EnviroTrac: Moved the garbage dumpsters back to 51/61 Cabot St. and 50 Dale St.; Moved metal construction material back to 61 Cabot St.; Moved the 40 Dale St. container back to its original location on the South Alleyway; Emptied the well development water down a 50 Dale St.

x - Designates report is continued on additional pages

CDM Site Representative: F. Robinson Project Manager: John Blaum

PHOTOGRAPHIC LOG

Date: 07/13/09

CDM Job No. D-006956

Spectrum Finishing Remedial Action

SITE No. 1-52-029

PHOTO	DATE	TIME	DESCRIPTION
100_0953.jpg	7/13/2009	AM	Setting up fence posts between 50 and 60 Dale St.
100_0954.jpg	7/13/2009	AM	40 Dale St. container moved back to it original location in the south alley
100_0955.jpg	7/13/2009	PM	Fence posts and top rails being installed, 61 Cabot St. in background

PHOTOS 7-13-09




100_0953.jpg - Setting up fence posts between 50 and 60 Dale St.



100_0954.jpg - 40 Dale St. container moved back to its original location in the south alley



100_0955.jpg - Fence post and top rails being installed, 61 Cabot St. in background

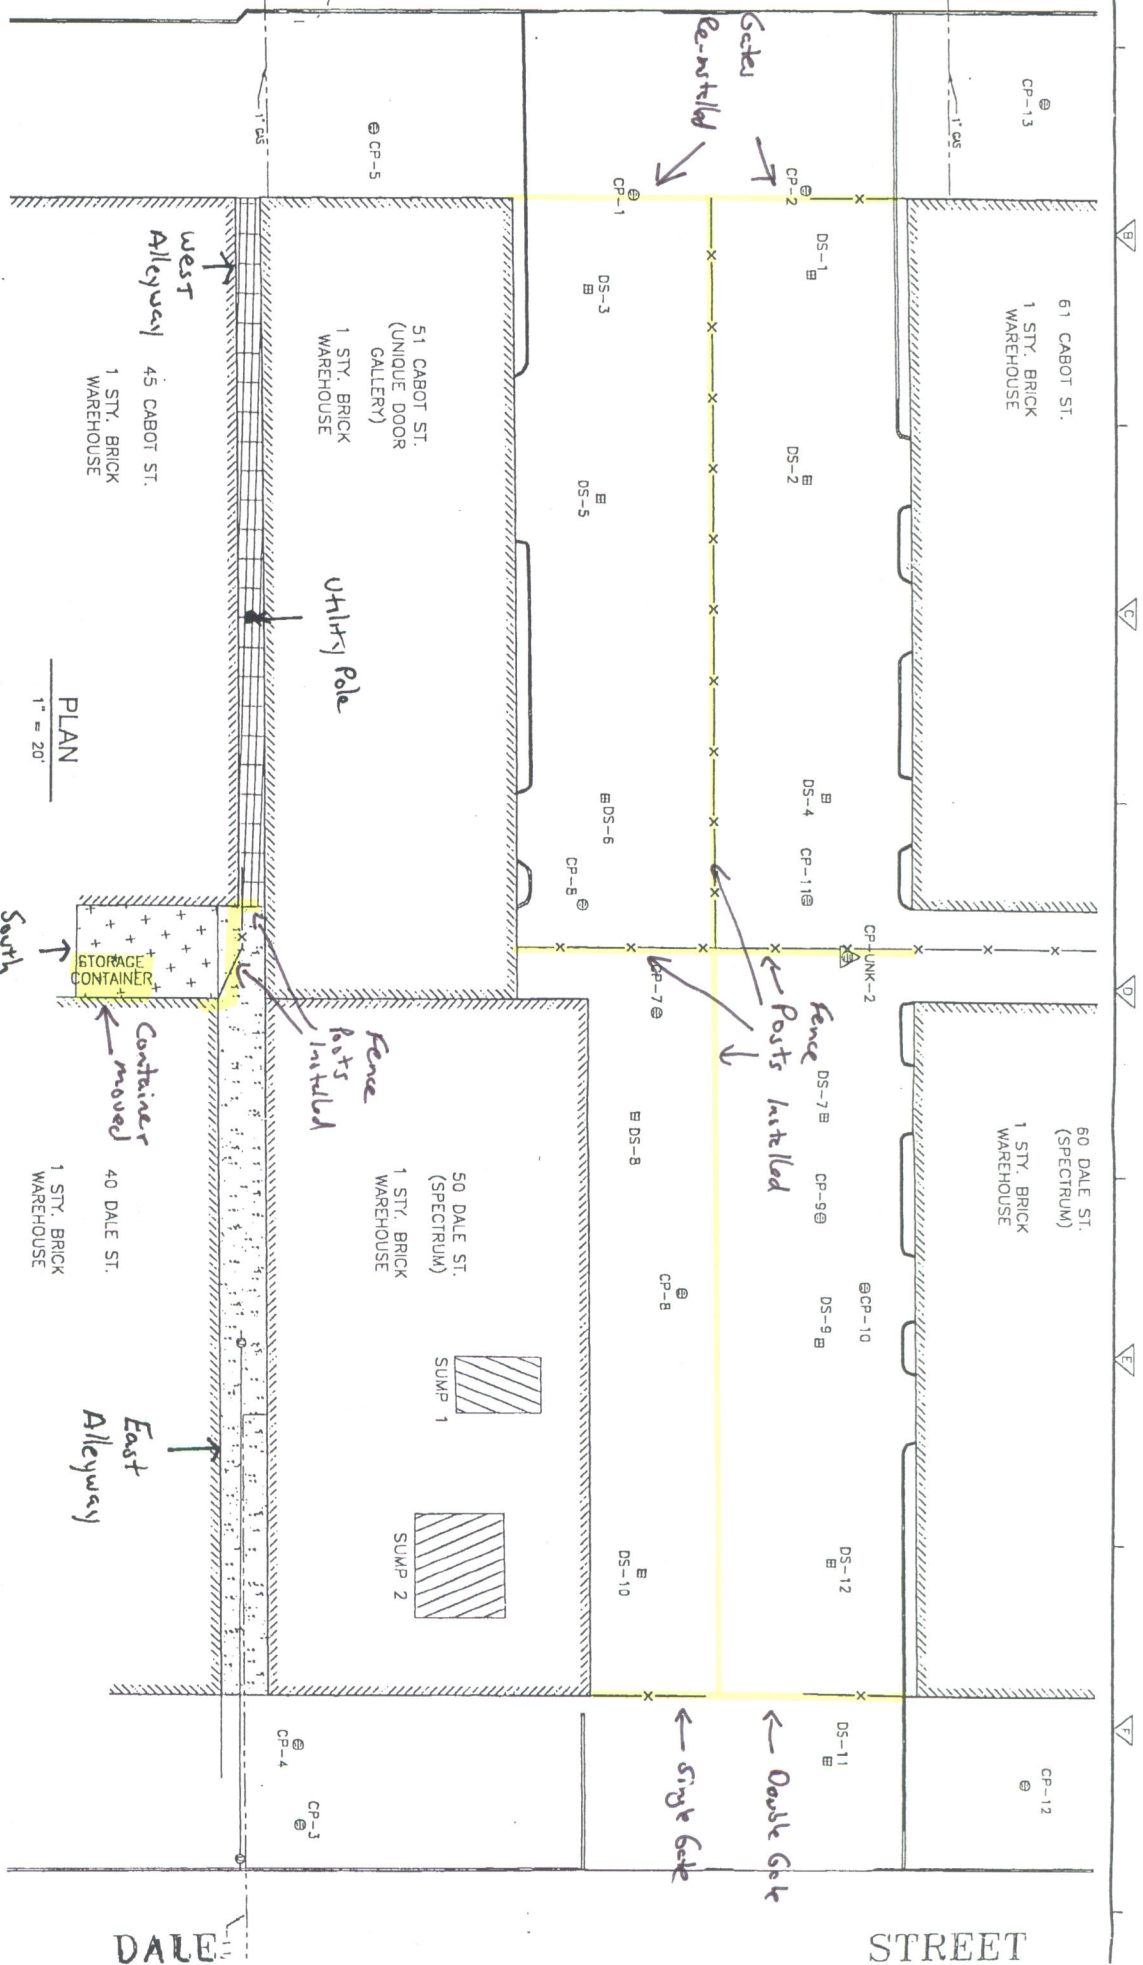

PLAN
1" = 20'

Work Areas

7/13/09

DALE

STREET
