

Daily Activity Report

Seton Brilla Charter School 1956 Jerome Avenue, Bronx, NY

BCP No. C203152

Genera	Cito	Infor	mation
Genera	Site	ши	IIIauoii

Date:	Thursday, March 2, 2023			
Weather:	Rain, 38-56°F			
Wind Direction/Speed:	NE @ 3 mph			
AKRF Personnel on Site:	Marcela Sanchez			
AKRF Equipment on Site:	Mini RAE 3000 Photoionization Detector [(PID) x1], 2 Fixed Air Monitoring Stations [DustTrak			
Visitors:	None.			

Contractor Information

Contractor information					
Contracting Company	Main Personnel	Equipment			
Casino Construction	Connor McGrory	Excavator, CFA Drill Rig			

Description and Location of Work Activities Performed

- 1) Soi/fill from grid WC-02 was excavated and sent for off-site disposal at the Clean Earth Bethlehem, PA facility.
- 2) Endpoint sample SW-11C_8-10_20230302 was collected from the north sidewall of the groundwater treatment area. The sample was submitted for laboratory analysis of petroleum VOCs.

 3) One truckload of 3/4

inch virgin bluestone from the Braen Stone Sparta Quarry was imported to the site as backfill for the groundwater treatment area excavation, and for use along the site boundary in WC-03.

Site Soil Disposal Tracking Information

Destination Facility	Daily Trucks	Total Trucks	Daily Approx. Cubic Yds	Total Approx. Cubic Yds	Total Site Loads	Total Approximate Cubic Yards
Clean Earth Carteret	0	73	0	1,460		
Clean Earth Southeastern Pennsylvania	1	67	20	1,340	166	3,320
Concrete Disposal	0	26	0	520		
N/A	0	0	0	0		
N/A	0	0	0	0		

CAMP Air Monitoring Results

CAMP Station	UPWIND			DOWNWIND			
Odors:	None.				None.		
VOC Action Level Exceedance(s):	NA				NA		
Particulate Action Level Exceedance(s):	NA				NA		
Maximum VOC Level (15 min ppm):	NA				NA		
Maximum Particulate Level (15 min mg/m³):	NA				NA		

Notes: CAMP and roving air monitoring were not performed due to inclement weather.


Additional Information

Planned Work Activity for Following Day/Week:

- 1) Excavation of soil/fill to uncover piles.
- 2) Cutting piles to final elevations

Comments:

None.

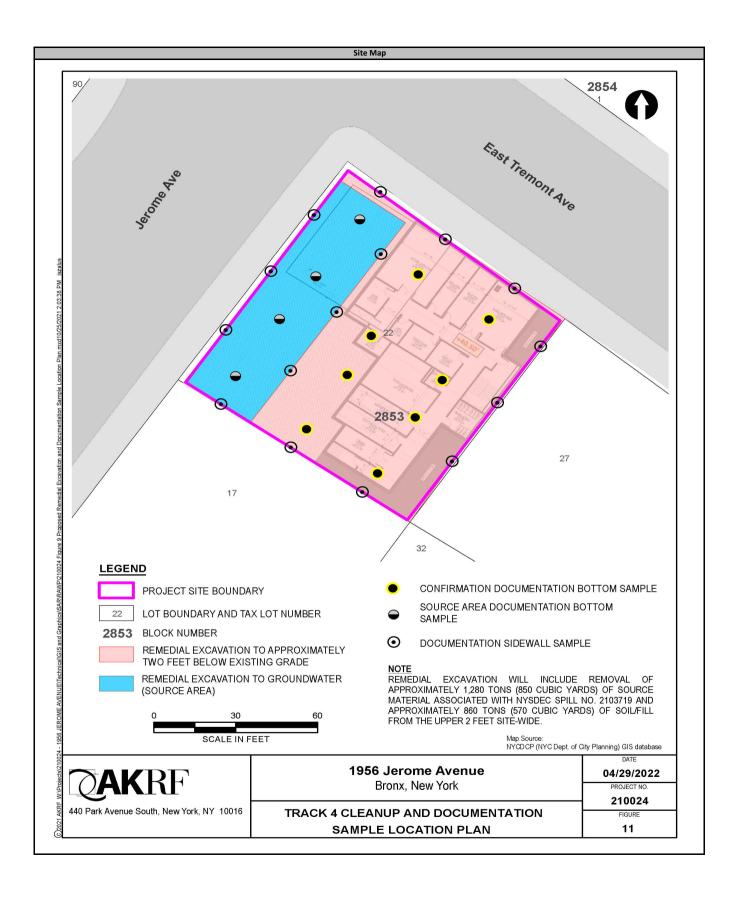

Site Photographs

Photograph 1 -Excavation in Grid WC-02 for endpoint sampling, view facing south.



Photograph 2- The excavator spreading 3/4-inch virgin bluestone in WC-02, view facing southwest.



Photograph 3-Excavation of soil against SOE wall in WC-03, view facing south.

