



Monthly Progress Report

Site Name: Franklin Cleaners
Site No.: 130050
Work Assignment No. D009809-18
MACTEC Project No. 3616206123
Report Month: July 2022
Report by: Katie Amann
Reviewed by: Chuck Staples

Section 1 – Accomplishments

Task 1 – Scoping

- N/A

Task 2 – Site Management Plan

- N/A

Task 3 – Operations and Maintenance

- Performed monthly inspection of the treatment building’s emergency lighting and fire extinguisher.

Task 4 – Monitoring and Reporting

- Conducted routine monthly reporting and management.

Task 5 – Remedial System Optimization

- N/A

Section 2 – Problems Encountered

None to report.

Section 3 – Progress Schedule Compliance

See attached schedule.

Section 4 – Potential Changes in Scope

None to report.

Section 5 – Planned Activities Next Month

Planned activities for August 2022:

- Perform monthly inspections of the treatment building’s emergency lighting and fire extinguisher.
- Provide PSEG access to electric meter at the treatment building for replacement.

Section 6 – Green/Sustainable Remediation

On-Going Efforts

- Local staff is utilized for routine site visits and carpooling is encouraged, when applicable, to minimize transportation impacts.


Future Efforts

- Green/sustainable remediation/climate resiliency evaluations will be incorporated into potential future investigations/studies at the site.

Section 7 – Cost Control

Task	Description	Budget	Spent to Date	% Complete
01	Scoping	\$13,661	\$14,487	Task Complete
02	Site Management Plan	\$9,041	\$0	0%
03	Operations and Maintenance	\$17,527	\$13,225	75%
04	Monitoring and Reporting	\$82,655	\$64,208	78%
05	Remedial System Optimization	\$6,742	\$0	0%

Franklin Cleaners Site - Site Management (Site 130050) - Work Assignment # D009809-18

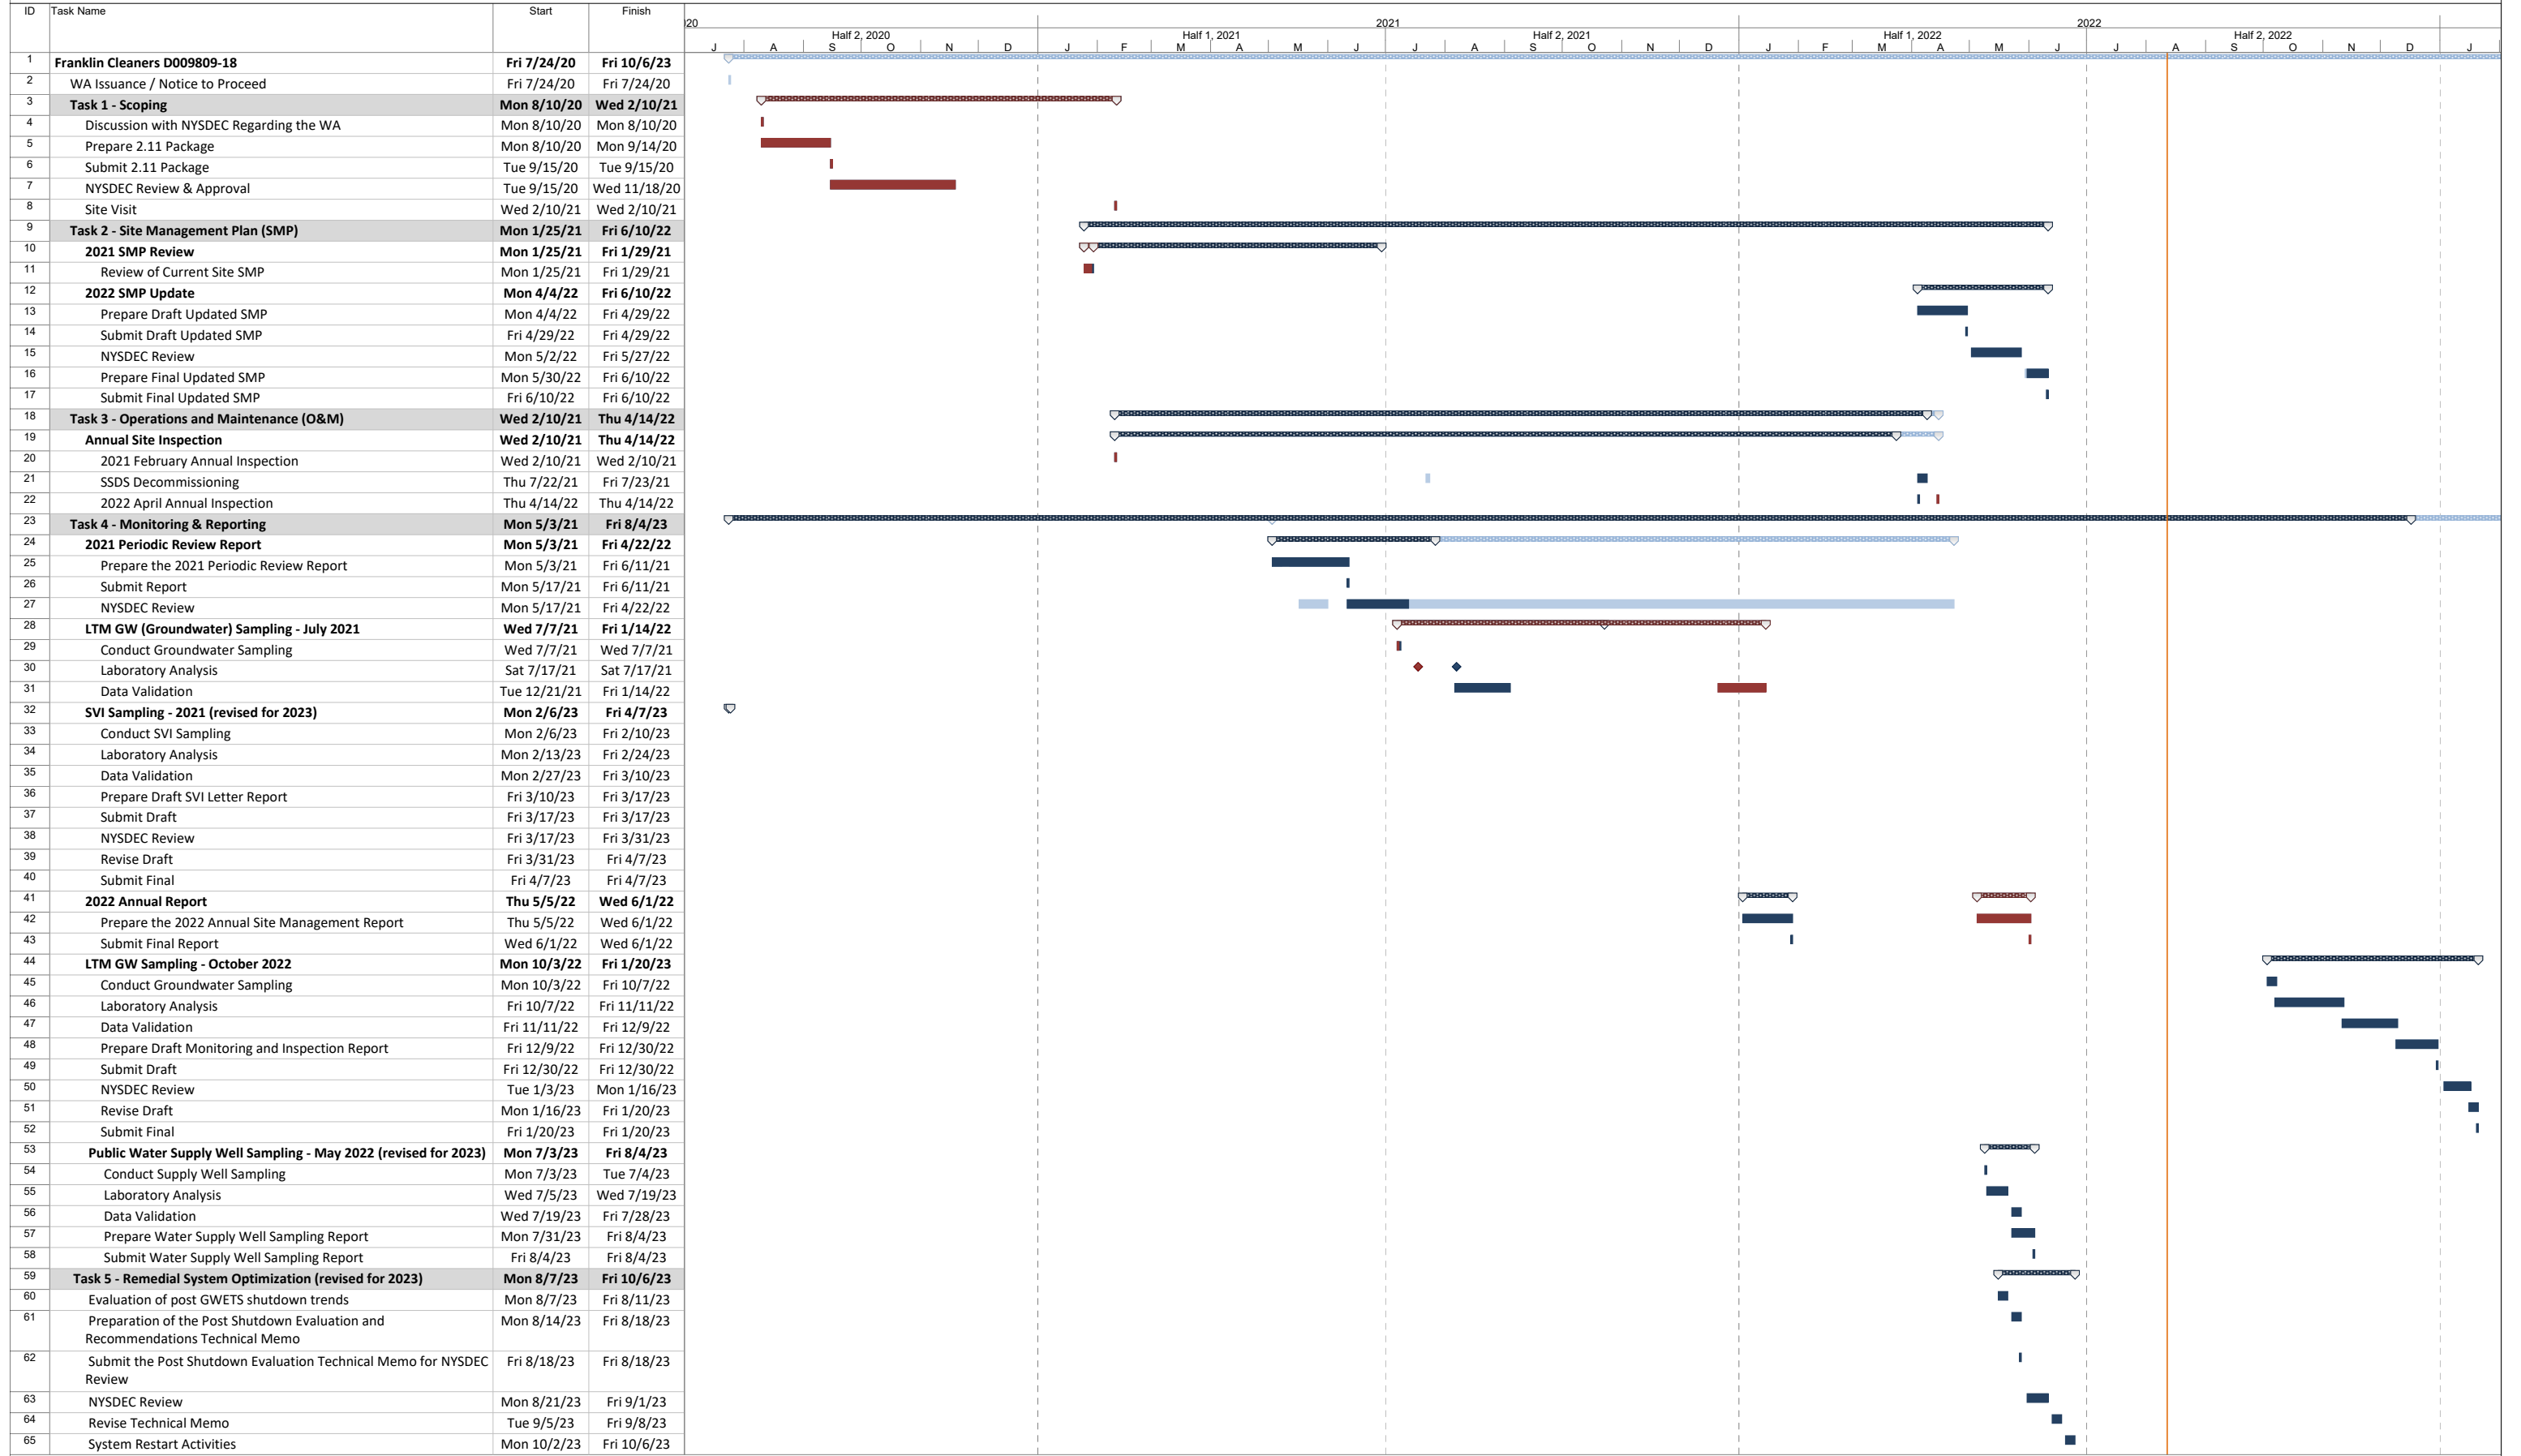

Project: D009809-18
Date: Fri 8/12/22

Revised Scheduled Summary Actual Summary Revised Milestone Date Original Milestone Date Actual Milestone Date
Originally Scheduled Summary Revised Task Dates Original Task Dates Actual Task Dates
