

January 7, 2004

Mr. Jeff Dyber, P.E.
Environmental Engineer 2
New York State Department of Environmental Conservation
Division of Environmental Remediation
Bureau of Eastern Remedial Action
625 Broadway
Albany, New York 12233

**RE: National Heatset Printing
Operation & Maintenance Report, December 2003
1 Adams Boulevard
Farmingdale, New York
NYSDEC Site 1-52-140**

Dear Mr. Dyber:

This letter provides an overview of the ongoing operation of the soil vapor extraction (SVE) system for the National Heatset Printing Site in Farmingdale, New York (**Figure 1**) for the reporting period including December 2003.

System Operation

Operation of SVE system began on September 17, 2002. The SVE system has been inactive for the entire reporting period pending the replacement of two blower control components. The system operational data collected to date is summarized in **Table 1**.

No water was collected from the knockout vessel during this reporting period. A small quantity of water has been collected during the previous reporting periods and placed in an accumulation drum for storage until the drum has been filled, at which time proper characterization and disposal procedures will be followed.

Monitoring Probes

Monitoring of the vapor monitoring points was not performed during December 2003. Monitoring of the vapor points will resume during future site visits.

PCE Removal

The SVE system has removed approximately 2,157 pounds of PCE to date. A summary of the estimated PCE mass removal over time is presented in **Table 2**.

Air Discharge Monitoring

Shaw personnel did not collect a sample of the system effluent air for laboratory analyses during December 2003. Sampling of the system effluent air stream will resume during future site visits. Air sample analytical results to date are presented in **Table 3**. A summary of field monitoring and laboratory air discharge monitoring results to date is presented as **Table 4**.

Conclusions and Recommendations

Shaw recommends continued operation of the SVE system at 1 Adams Boulevard. As site conditions change, adjustments will be made to optimize the system operation. The system is currently idle, but will be restarted as soon as possible upon the receipt and installation of replacement blower control components.

Please do not hesitate to contact me at 518-783-1996 with any questions you might have regarding this report.

Sincerely,
Shaw Environmental, Inc.



John A. Skaarup
Project Engineer

Cc: File

Attachments: Tables
Figures

TABLES

TABLE 1

SUMMARY OF SOL VAPOR EXTRACTION SYSTEM READINGS
 NATIONAL HEATSET PRINTING
 1 ADAMS BLVD., FARMINGDALE, NY

Date	Run Time Meter Reading (hours)	Run Time Since Last Visit (hours)		Operation Time Since Last Visit (%)	Dilution Valve Position (% Open)	Extraction Well MW-F Valve Position (% Open)	Air Flow at Well (scfm)	Vacuum at Well (inches H2O)	Pre-Dilution PID (ppm)	Pre-Dilution PCE (ppm)	Influent SVE				Mid GAC				Effluent GAC					
		Available	Actual								Blower Flow (cfm)	Vacuum (inches H2O)	Temp. (°F)	PID (ppm)	PCE (ppm)	Flow (cfm)	Temp. (°F)	PID (ppm)	PCE (ppm)	Flow (cfm)	Temp. (°F)	PID (ppm)	PCE (ppm)	
9/18/2002	--	--	--	--	--	--	--	--	--	--	SVE PILOT TEST STARTUP													
9/30/2002	304	294	/	294	100%	100	50	34.5	5	2,000	500	256	25	107.2	1,015	--	317	102.3	0	--	290	89.5	0	--
10/14/2002	642	343	/	338	99%	100	50	38	7	1,011	400	258	27	--	75.3	50	--	--	0	--	--	--	0	--
11/19/2002	1508	882	/	866	98%	100	50	49	12	0	0	120	28	106	0	0	209	92	0	--	290	80.3	0	--
12/4/2002	--	368	/	--	--	--	--	--	--	77	200	--	--	--	14.3	10	--	--	15.5	10	--	--	0	0
12/16/2002	2153	294	/	645	98%	100	50	36.5	10	560	200	253	28	92	46.4	50	302	60	3.4	--	340	53.9	0	--
1/21/2003	3016	882	/	863	98%	100	50	--	--	--	--	70	52	98	0	0	220	--	0	--	220	--	0	--
2/10/2003	3496	490	/	480	98%	100	50	38	--	639	400	262	27	102	72	50	266	90	26	10	258	83	3.2	10
3/18/2003	4360	882	/	864	98%	100	50	92	12	125	100	266	25	123	15	10	278	124	0	0	282	117	0	0
4/29/2003	5359	1029	/	999	97%	75	50	75	50	152	50	132	16	118.5	48.2	25	302	96	18.6	10	287	86	0.6	0
5/13/2003	5700	343	/	341	99%	75	50	78	--	127	50	239	48	130	41.8	50	246	108	46	25	245	97	0.6	0
6/30/2003	6850	1176	/	1150	98%	50	50	115	32	82.4	50	140	66	173	36.8	50	198	157	25.1	25	240	150	29.8	100
7/10/2003	6851	245	/	1	0%	50	50	99.5	25	406	400	151	68	156	221	215	260	76	0	0	222	81.9	0	0
7/22/2003	7144	294	/	294	100%	50	50	--	--	127	--	--	--	168	65	--	--	107	0	--	--	106	0	--
8/26/2003	7957	858	/	813	95%	50	50	79	13.5	137	10	186	65	170	51.4	5	291	--	55.4	10	232	--	35.6	10
9/23/2003	8274	686	/	317	46%	50	50	218	33	141	15	194	64	160	55	30	254	124	0	0	210	110	0	0
10/21/2003	8945	686	/	671	98%	50	50	166	45	--	20	158	68	166	37.5	25	214	130	30.7	15	225	112	0	0
11/24/2003	9749	833	/	805	97%	50	50	130	46	141	125	178	72	138	261	200	225	52	0	0	205	51.4	0	0

Notes:
 PID = Total VOC concentration measured with photoionization detector
 ppm = parts per million (volume/volume basis)
 PCE = Tetrachloroethene (PCE) concentration measured with Drager tube of 10-500 ppm range
 scfm = standard cubic feet per minute
 cfm = cubic feet per minute
 Influent SVE = Readings collected between the SVE Blower and the Carbon Units
 Mid GAC = Readings collected between the lead and lag carbon units
 Effluent GAC = Readings collected after the lag carbon unit
 GAC = granular activated carbon unit
 -- = measurement not recorded

TABLE 2
PCE
REMOVAL ESTIMATE
NATIONAL HEATSET PRINTING
1 ADAMS BLVD., FARMINGDALE, NY

Date	VOC Influent Concentration* (ppmv)	PCE Influent Concentration* (ppmv)	% PCE of Total VOCs	Extraction Well Flow Rate (cfm)	Elapsed Time Since Last Visit (day)	PCE Removal Since Last Visit (lb)	Cumulative PCE Removal (lb)
9/18/2002	SVE PILOT TEST STARTUP						
9/30/2002	2,000	500	25.0	34.5	12	126	126
10/14/2002	1,011	400	39.6	38	14	129	255
11/19/2002	0	0	--	49	36	116	371
12/16/2002	560	200	35.7	36.5	27	70	441
1/13/2003	485	400	82.5	28.5	28	157	597
1/21/2003	0	0	--	0	8	63	660
2/10/2003	639	400	62.6	38	20	65	725
3/5/2003	263	200	76.0	24.4	23	132	856
3/18/2003	125	100	80.0	92	13	77	934
4/29/2003	152	50	32.9	75	42	109	1,042
5/13/2003	127	50	39.4	78	14	65	1,107
6/30/2003	82.4	50	60.7	115	48	91	1,198
7/22/2003	406	400	98.5	99.5	12	416	1,615
8/26/2003	137	10	7.3	79	35	291	1,906
9/23/2003	141	15	10.6	218	14	30	1,936
10/21/2003	37.5	20	53.3	166	28	42	1,978
11/24/2003	141	125	88.7	130	34	179	2,157

Notes:

* = VOC concentrations of 2,000 ppm and PCE concentrations of 500 ppm are greater than the limit of their respective monitoring device and are to be taken as estimations.

Removal Rate = [(flow(cfm)*influent conc.(ppmv)*MW*12.187)/(273.15+C)]*1 cu. m./35.31 cu. ft*1g/1000 mg*1 lb/453.6 g*60 min/1 hr*24 hr
*days of operation

Where:

MW = molecular weight

Molecular weight (MW) of PCE is 165.85

C = degrees centigrade, assumed to be 25

lb = pounds

cfm = cubic feet per minute

ppmv = parts per million (volume/volume basis)

TABLE 3

**AIR SAMPLE ANALYTICAL RESULTS
NATIONAL HEATSET PRINTING
1 ADAMS BLVD., FARMINGDALE, NY**

SVE Influent Concentration (mg/m3)			
Date	cis-1,2-Dichloroethene	Tetrachloroethene (PCE)	Trichloroethene
9/18/2002	5	600E	31
9/30/2002	ND (5)	360E	23
10/14/2002	--	--	--
11/19/2002	--	--	--

VGAC Effluent Concentration (mg/m3)			
Date	cis-1,2-Dichloroethene	Tetrachloroethene (PCE)	Trichloroethene
9/18/2002	--	--	--
9/30/2002	--	--	--
10/14/2002	--	--	--
11/19/2002	--	--	--
12/16/2002	ND (5)	ND (5)	ND (5)
1/21/2003	--	--	--
2/10/2003	ND (5)	8	6
3/18/2003	--	--	--
4/29/2003	--	--	--
5/13/2003	ND (1)	5	ND (1)
6/30/2003	--	--	--
7/22/2003	ND (1)	ND (1)	ND (1)
8/26/2003	ND (5)	29	3.6
9/23/2003	ND (5)	ND (5)	ND (5)
10/21/2003	ND (5)	ND (5)	ND (5)
11/24/2003	--	--	--

Notes:

Only compounds that were detected above the method reporting limit were presented above

ND(5) = Not detected above method reporting limit in parenthesis

E = Concentration exceeded calibration range

SVE = Soil vapor extraction

VGAC = vapor-phase granular activated carbon unit

mg/m3 = milligrams per cubic meter

-- = sample not collected

TABLE 4

**AIR DISCHARGE MONITORING
NATIONAL HEATSET PRINTING
1 ADAMS BLVD., FARMINGDALE, NY**

Date	Field Monitoring				Laboratory Results		Discharge based on Field Monitoring		Discharge based on Laboratory Results			
	System Effluent Flow Rate (cfm)	PCE System Effluent Concentration (ppmv)	System Effluent VOC Concentration (ppmv)	Elapsed Time (day)	PCE (mg/cu m.)	TCE (mg/cu m.)	PCE Discharge Since Last Visit (lb/hr)	PCE Discharge Since Last Visit (lb)	PCE Discharge Since Last Visit: lb/hr	PCE Discharge Since Last Visit (lb)	TCE Discharge Since Last Visit (lb/hr)	TCE Discharge Since Last Visit (lb)
9/18/2002	SVE PILOT TEST STARTUP											
9/30/2002	290	--	0	12	--	--	--	--	--	--	--	--
10/14/2002	--	--	0	14	--	--	--	--	--	--	--	--
11/19/2002	290	--	0	36	--	--	--	--	--	--	--	--
12/16/2002	340	--	0	27	ND (5)	ND (5)	--	--	0.00	0.00	0.00	0.00
1/13/2003	45	0	--	28	--	--	0.0000	0.00	--	--	--	--
1/21/2003	220	--	0	8	--	--	--	--	--	--	--	--
2/10/2003	258	10	3.2	20	8.0	6.0	0.0654	31.40	0.008	3.71	0.006	2.78
3/5/2003	305	--	0	23	--	--	--	--	--	--	--	--
3/18/2003	282	0	0	13	--	--	0.0000	0.00	--	--	--	--
4/29/2003	287	0	0.6	42	--	--	0.0000	0.00	--	--	--	--
5/13/2003	245	0	0.6	14	5.0	ND (1)	0.0000	0.00	0.005	1.54	0.00	0.00
6/30/2003	240	100	29.8	48	--	--	0.3043	350.56	--	--	--	--
7/22/2003	222	--	0	12	ND (1)	ND (1)	--	--	0.00	0.00	0.00	0.00
8/26/2003	232	10	35.6	35	29.0	3.6	0.0588	49.42	0.025	21.17	0.003	2.63
9/23/2003	210	0	0	28	ND (5)	ND (5)	0.0000	0.00	0.000	0.00	0.000	0.00
10/21/2003	225	0	0	28	ND (5)	ND (5)	0.0000	0.00	0.000	0.00	0.000	0.00
11/24/2003	205	0	0	34	--	--	0.0000	0.00	--	--	--	--
Totals:								431.38		26.42		5.41

Notes:

-- = Measurement not recorded

*: Total VOC Discharge = PCE lab result + TCE lab result

Discharge Rate (Field Monitoring, lb/hr) = [(flow(cfm)*influent conc.(ppmv)*MW*12.187)/(273.15+C)]*1 cu. m./35.31 cu. ft*1g/1000 mg*1 lb/453.6 g*60 min/1 hr

Discharge (lb) = Discharge Rate (lb/hr) * # of days*24hours/day*60 minutes/hr

Discharge Rate (Lab Results, lb/hr) = flow (cfm)*effluent conc. (mg/cu. m.)*1g/1000mg*1lb/453.6g*1cu. m./35.31cu. ft*60min/1 hr

Discharge (lb) = Discharge Rate (mg/cu. m) * # of days*24hours/day*60 minutes/hr

Where:

MW = molecu

Molecular weight (MW) of PCE is 165.85, Molecular weight (MW) of TCE is 131.4

C = degrees centigrade, assumed to be 25

cfm = cubic feet per minute

mg/cu. m = milligrams per cubic meter


ppmv = parts per million (volume/volume basis)

lb = pounds

hr = hours

Permit Limit		
	lb/hr	lb/yr
PCE	0.031	270
TCE	0.014	120

FIGURES

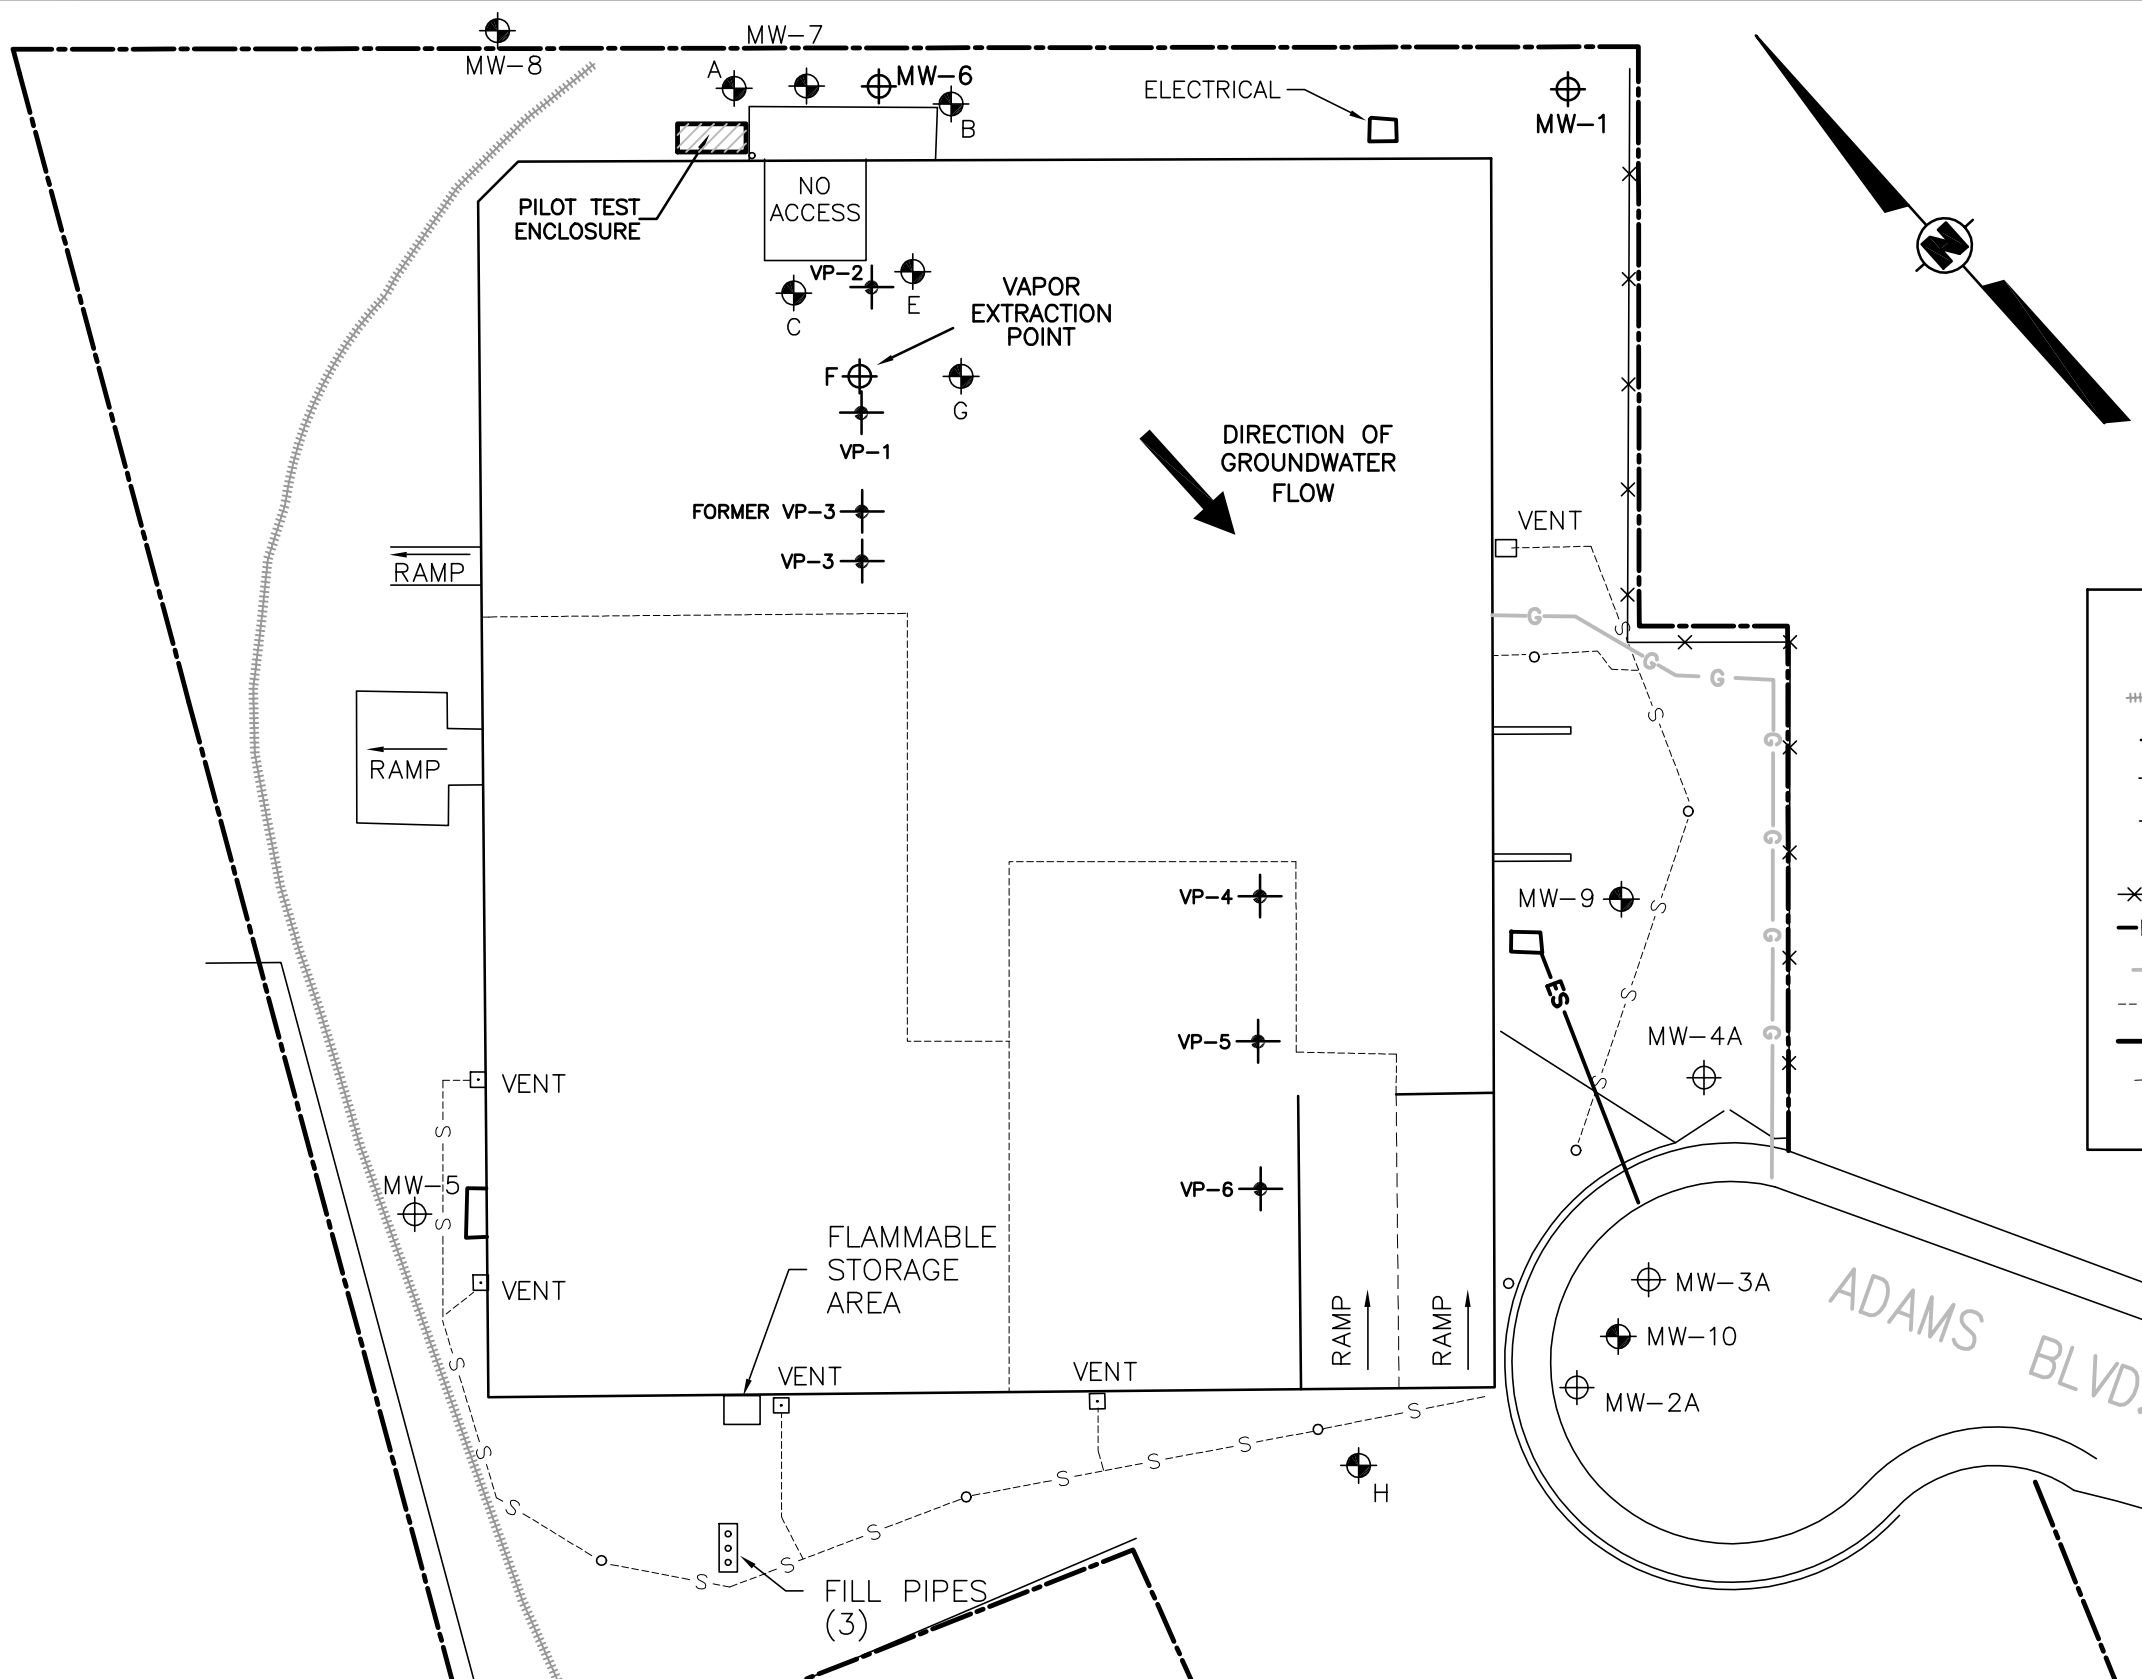

LEGEND:

- +++++ TRAIN TRACK
- ⊕ VAPOR MONITORING POINT
- ⊙ DEEP MONITORING WELL (>30')
- ⊕ SHALLOW MONITORING WELL (<30')
- MANHOLE OR ACCESS POINT
- ×× FENCE LINE
- ES- ELECTRIC LINE
- G- GAS LINE
- S- SANITARY SEWER
- PROPERTY LINE
- INTERIOR BUILDING WALL (DIVIDES WAREHOUSE)

FIGURE 1

	NATIONAL HEATSET PRINTING FARMINGDALE, NEW YORK			
	SOIL VAPOR EXTRACTION PILOT TEST LOCATION MAP			
DESIGNED BY	J. SKAARUP	10/23/02	CHECKED BY	
DRAWN BY	CA/HMD/SSH	10/23/02	APPROVED BY	
SCALE:	AS SHOWN	DRAWING NO.	802901B35	SHEET NO.
				REVISION NO.
				4

REV	DATE	BY	CHK'D	APR'VD	DESCRIPTION/ISSUE
4	6/9/03	SSH			UPDATE DRAWING
3	4/17/03	SSH			UPDATE DRAWING
2	1/16/03	SSH			ADD FORMER VP-3 TO DRAWING
1	12/3/02	SSH			UPDATE DRAWING
