

Project	Bedford Beverly Brownfield	Report No.	44	
-	Site			
BCP Site	BCP Site No. C224384	Date	12/07/2023	
Location	2359 and 2360 Bedford	File No. 0205432		
	Avenue, Brooklyn, NY			
Client	Bedford Beverly Acquisitions	Temperature	31-40 °F	
	LLC, Maman Contracting			
	(Maman), International			
	Concrete			
Contractor	Haley & Aldrich	Wind Direction	SW to NE, 9 mph	
Weather	Mostly Cloudy with snow	Personnel on	E. Nunez & D. Djombalic	
	flurries	Site		
Humidity	68%	Time on Site	6:30 am to 3:45 pm	

Haley & Aldrich of New York (Haley & Aldrich) was present to document implementation of the Remedial Action Work Plan (RAWP) prepared by Haley & Aldrich currently under review by NYSDEC and the NYSDEC-approved Change of Use dated 17 August 2023 to begin support of excavation work. Site observations are summarized below.

Daily Observations:

- Contractor (International Concrete) continued support of excavation (SOE) prep along the perimeter of Lot 14 and stockpiled soil in preparation for disposal.
- Contractor (International Concrete) continued loading soil for transport and disposal off-site.

Waste Disposal/Backfill Import Tracking:

Material Export:

- Seventy-two (72) loads of non-hazardous fill material from grids WC-04 (10-15'), WC-03 (10-15'), and WC-02 (10-15').
- Soil/Fill disposal is summarized below:

	Facility:	Bayshore	Facility: P Park NJ		Facility: Keystone		Facility: Posillico					
	Soil Mar	nagement,	LLC, Prospect Park,		Trade Center,		Materials Permitted					
	Keasbey	, NJ (Non-	NJ (Non-Haz Soil)		Fairless Hills, PA		Wash Plant, LLC,					
	Haz	: Soil)			(Non-Haz Soil)		Farmingdale, NY		Totals:			
							(Non-Haz Soil)					
Today:	0 Loads	0 CY	72 Loads	1,440 CY	0 Loads	0 CY	0 Loads	0 CY	72 Loads	1,440 CY		
<u>Total:</u>	<u>154</u> Loads	<u>3,080 CY</u>	<u>267</u> Loads	<u>5,340 CY</u>	<u>171</u> Loads	<u>3,420 CY</u>	87 Loads	<u>1,740 CY</u>	<u>679</u> Loads	<u>13,580</u> <u>CY</u>		

*Note, 1 truck estimated at 20 cubic yards. Final tonnages will be present in the Final Engineering Report (FER)



 Asphalt disposal is summarized below: 								
	Facility: Flusl Recycling, F (Aspl	lushing NY	Facility: Materials, F PA (As		Tota	ıls:		
Today:	0 Loads	0 CY	0 Loads	0 CY	0 Loads	0 CY		
<u>Total:</u>	117 Loads	<u>2,340 CY</u>	<u>9 Loads</u>	<u>180 CY</u>	126 Loads	<u>2,520 CY</u>		

*Note, 1 truck estimated at 20 cubic yards. Final tonnages will be present in the Final Engineering Report (FER)

• C&D disposal is summarized below:

	Facility: Mate Fairless I	rials,			
	(Non-Haz	,	Totals:		
Today:	0 Loads 0 CY		0 Loads	0 CY	
<u>Total:</u>	51 Loads	<u>1,020 CY</u>	<u>51 Loads</u>	<u>1,020 CY</u>	

*Note, 1 truck estimated at 20 cubic yards. Final tonnages will be present in the Final Engineering Report (FER)

Material Import:

• Material import is summarized below:

	Facility: Mo	ount Hope	Facility: M	ount Hope		
	Qua	rry,	Qua	arry,		
	Wharton, NJ (ASTM #57)		Whart	ton, NJ		
			(ASTI	M #3)	Totals:	
Today:	0 Loads	0 CY	0 loads	0 CY	0 Loads	0 CY
<u>Total:</u>	<u>5 Loads</u>	<u>100 CY</u>	<u>11 loads</u>	<u>220 CY</u>	<u> 16 Loads</u>	<u>320 CY</u>

*Note, 1 truck estimated at 20 cubic yards. Final tonnages will be present in the Final Engineering Report (FER)

Samples Collected:

• No samples were collected.

CAMP Activities:

 Air monitoring during ground-intrusive activities was performed at two locations during ground intrusive work from 7:00 am to 3:30 pm. No 15-minute average concentration of volatiles organic compounds (VOCs) or particulate 15-minute average concentration of matter smaller than 10 microns in diameter (PM10) exceeded the action levels. No visible dust was observed leaving the site perimeter.



Activities Planned for Coming Week:

- Contractor (International Concrete) will continue stockpiling soil on the perimeter of Lot 14 for disposal.
- Contractor (International Concrete) will continue installing H piles as part of SOE installation on the perimeter of the site.
- Contractor (International Concrete) will continue transportation and disposal of soil/fill to an approved facility.



Site Photographs:

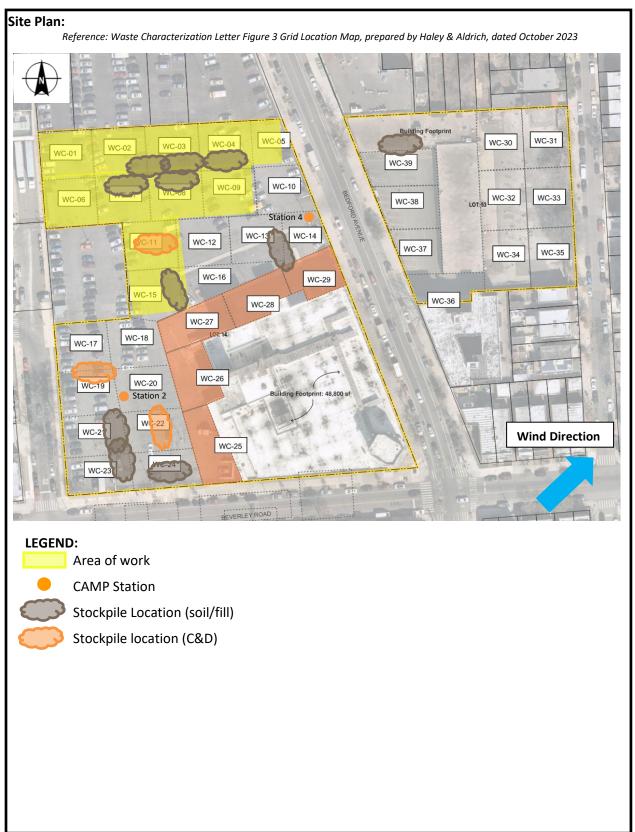


Photo 1: View of contractor loading soil on Lot 14, facing northwest.



Photo 2: View of contractor loading soil on Lot 14, facing northwest.





2360 Bedford Avenue, Brooklyn NY

Air Monitoring Log

Date: 2023-12-07

Personnel :	D. Djombalic & E. Nunez
Weather :	Mostly Cloudy
Humidity :	68%
Wind Direction :	SW to NE, 9 mph

Particulate Background (ug/m3) : <u>3.295</u> PID Background (ppm) : <u>0.0</u>

Action Levels : Downwind perimeter of work area above background levels

PID (ppm) :> 5 ppm for the 15-min average

Dust (ug/m3) : > 150 for the 15-min average

Minute of Time	Avg. PM10 (Station1)	Avg. PM10 (Station2)	Avg. PM10 (Station3)	Avg. PM10 (Station4)	Avg. VOC(Station1)	Avg. VOC(Station2)	Avg. VOC(Station3)	Avg. VOC(Station4)	Odors	Notes Activities/ Additional Monitoring
07:00		3.295		6.781		0.0		0.0		
07:15		2.770		5.444		0.0		0.0		
07:30		2.736		7.260		0.0		0.0		
07:45		2.679		4.620		0.0		0.0		
08:00		2.763		4.432		0.0		0.0		
08:15		3.110		4.697		0.0		0.0		
08:30		3.370		4.825		0.0		0.0		
08:45		3.847		4.423		0.0		0.0		
09:00		4.024		5.267		0.0		0.0		
09:15		3.987		5.717		0.0		0.0		
09:30		4.273		6.068		0.0		0.0		
09:45		4.594		5.568		0.0		0.0		
10:00		4.031		5.046		0.0		0.0		
10:15		4.541		5.063		0.0		0.0		
10:30		4.982		5.947		0.0		0.0		
10:45		5.119		6.956		0.0		0.0		

2360 Bedford Avenue, Brooklyn NY

Air Monitoring Log

Minute of Time	Avg. PM10 (Station1)	Avg. PM10 (Station2)	Avg. PM10 (Station3)	Avg. PM10 (Station4)	Avg. VOC(Station1)	Avg. VOC(Station2)	Avg. VOC(Station3)	Avg. VOC(Station4)	Odors	Notes Activities/ Additional Monitoring
11:00		5.233		7.0		0.0		0.0		
11:15		5.473		7.3		0.0		0.0		
11:30		5.476		7.6		0.0		0.0		
11:45		5.829		7.3		0.0		0.0		
12:00		5.652		7.4		0.0		0.0		
12:15		5.978		7.2		0.0		0.0		
12:30		5.423		6.9		0.0		0.0		
12:45		5.506		8.4		0.0		0.0		
13:00		5.996		9.0		0.0		0.0		
13:15		6.097		7.7		0.0		0.0		
13:30		6.324		8.6		0.0		0.0		
13:45		7.081		8.4		0.0		0.0		
14:00		7.995		13.1		0.0		0.0		
14:15		8.724		10.4		0.0		0.0		
14:30		9.178		11.0		0.0		0.0		
14:45		11.536		11.0		0.0		0.0		
15:00		9.921		10.8		0.0		0.0		
15:15		10.184		10.5		0.0		0.0		
15:30		10.207				0.0				
