

SITE OBSERVATION REPORT

PROJECT No.: 170381202

CLIENT:

LLC

DATE: Tuesday, September 5, 2023

PROJECT:

250 Water Street

Partly Sunny, 80 – 92° F

WEATHER:

Wind: SE @ 0.2 – 1.7 mph

LOCATION:

New York, NY

TIME:

5:45am - 5:15pm

BCP SITE ID:

C231127

MONITOR

Jack Millman

EQUIPMENT:

CAT 335 Excavator CAT 328 Excavator

Komatsu PC138 Excavator

Delmag Drill Rig Bauer RTG RG 27S Bauer BG45 Drill Rig

Jerome J505 Mercury Vapor Analyzer RKI GX-6000 Photoionization Detector (PID) Aeroqual ASQ1 Air Monitoring Station

PRESENT AT SITE:

250 Seaport District,

Hughes Corporation

c/o The Howard

Day 196 Langan (Environmental/Geotechnical) Jack Millman, Michael Cole,

Pepper Greenley, Pradeep Pandey

Suffolk Construction (Suffolk) (General Contractor) Anthony Galu,

Wyatt Favia

East Coast Drilling, Inc. (ECD) (Foundation Contractor) Danny Rodgers

New York State Department of Environmental Conservation

(NYSDEC) Mike Sollecito

OBSERVATIONS, DISCUSSIONS, TEST RESULTS, ETC.:

Langan was present to document remediation activities in accordance with the NYSDEC-approved November 2021 Remedial Action Work Plan (RAWP) at the 250 Water Street site (NYSDEC Brownfield Cleanup Program [BCP] Site No C231127).

Site Activities

- ECD used a Bauer RTG RG 27S drill rig to pre-drill one borehole in the eastern part of the site to loosen the underlying soil in preparation for soil mix column installation.
- ECD used a Bauer BG45 drill rig to install two deep soil mix columns for support-of-excavation (SOE) installation in the eastern part of the site (along Peck Slip Street). ECD's drill rig advanced a steel rod with two cutter blades at the bottom of the rod, while concurrently injecting grout through the cutting head and spinning and advancing the blades downward to a depth of about 79 feet below grade surface (bgs).
 - No drilling spoils were generated during installation of the soil mix column.
 - o Excess grout was contained within a temporary containment area in the eastern part of the site and will be managed as construction and demolition (C&D) debris at a later date.
- ECD excavated an about 5-foot-long by 15-foot-wide area to a maximum depth of about 6 feet bgs in the southern part of the site (waste characterization cell WC06) to identify potential obstructions prior to SOE installation.
 - o Excavated soil/fill was screened for odors, staining, organic vapors, and mercury vapor using a handheld photoionization detector (PID) and handheld Jerome® J505 mercury vapor analyzer, respectively. No evidence of impacts was observed and the excavated soil/fill was temporarily backfilled into the original location following removal of concrete obstructions.
 - Atmos® AC-645 odor/vapor suppressing foam was actively applied to the soil/fill during excavation as a precautionary measure.

Cc: M. Raygorodetsk	y, P. McMahon, M. Au, J. Frey,	Ву:	Jack Millman
S. Simpson			LANGAN



Page 2 of 7

SITE OBSERVATION REPORT

Material Tracking

- No material was exported from the site.
- No material was imported to the site.

Material Import Summary								
Facility Name Location Type of Material	Hal 1.5/2.5	ndustries, Inc. edon, NJ 5-inch Virgin Stone	Stone Industries, Inc. Haledon, NJ 0.75-inch Virgin Stone		Impact Reuse & Recovery Center or Impact Materials Jersey City, Lyndhurst/Jersey City, NJ 1.5-inch Clean Bluestone		Impact Reuse & Recovery Center, Lyndhurst, NJ General Fill	
Quantities	No. of Loads	Approx. Volume (Tons)	No. of Loads	Approx. Volume (Tons)	No. of Loads	Approx. Volume (Tons)	No. of Loads	Approx. Volume (Tons)
Today	0	0	0	0	0	0	0	0
Project Total	12	283.91	0	0	15	339.65	374	9,157.85
NYSDEC Approved:		1,800	tons*		72	20 tons*	19,500	tons*

*0.75-inch, 1.5-inch, and 2.5-inch virgin stone from the Stone Industries, Inc. facility and 1.5-inch clean bluestone from the Impact Reuse & Recovery Center (IRRC) facility were approved for import of 1,000 cubic yards (CY) and 400 CY, respectively. Assuming a conversion factor of 1.8, each quantity was converted to tons in order to accurately compare with import weight tickets. General fill from the IRRC facility was approved for import of 13,000 CY and a conversion factor of 1.5 is applied.

Material Export Summary (1 of 3)								
Facility Name Location Type of Material	Brook Construction	Recycling klyn, NY n & Demolition) Debris	IRRC Lyndhurst, NJ C&D Debris		Earth Efficient MSM East Stroudsburg, PA C&D Debris		Clean Earth of North Jersey Kearny, NJ Hazardous Lead-Impacted Soil/Fill	
Quantities	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)
Today	0	0	0	0	0	0	0	0
Project Total	5	85	42	840	28	560	95	1,900

	Material Export Summary (2 of 3)						
Facility Name Location Type of Material	Middlesex County Landfill East Brunswick, NJ Non-hazardous Soil/Fill		Keas	oil Management Bbey, NJ mpacted Soil/Fill	Clean Earth of Carteret, NJ Carteret, NJ Non-hazardous Soil/Fill		
Quantities	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	No. of Loads	Approx. Volume (CY)	
Today	0	0	0	0	0	0	
Project Total	273	5,460	267	5,340	66	1,320	

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey,	Ву:	Jack Millman
	S. Simpson		LANGAN



Page 3 of 7

SITE OBSERVATION REPORT

Material Export Summary (3 of 3)				
Facility Name Location Type of Material	Clean Earth of North Jersey Kearny, NJ Non-hazardous Soil/Fill			
Quantities	No. of Loads	Approx. Volume (CY)		
Today	0	0		
Project Total	201	4,020		

<u>Sampling</u>

•	No	samp	les '	were	col	lec1	ted.
---	----	------	-------	------	-----	------	------

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey,	Ву:	Jack Millman
	S. Simpson		LANGAN



Page 4 of 7

SITE OBSERVATION REPORT

CAMP Activities

Langan performed air monitoring at the perimeter of the site, at the northern sidewalk of Pearl Street, at the western sidewalk of Beekman Street, at the eastern sidewalk of Peck Slip, and at the southern sidewalk of Water Street at eight total locations for mercury vapor, volatile organic compounds (VOCs), and particulate matter less than 10 microns in diameter (PM10) from about 6:52am to 4:12pm. There were no fifteen-minute average concentrations for mercury vapor, VOCs or PM10 that approached or exceeded the action levels established by the CAMP (1.00 μ g/m³, 5.0 ppm, or 0.100 mg/m³, respectively).

Background Concentrations

Prior to implementation of CAMP, instantaneous background concentrations of mercury vapor and VOCs were recorded using a handheld Jerome[®] J505 mercury vapor analyzer and a handheld PID, respectively.

- Background concentrations of mercury vapor at each CAMP station were recorded at 0.00 μg/m³.
- Background concentrations of VOCs at each CAMP station were recorded at 0.0 ppm.

Perimeter and Work Zone Concentrations

Daily Average Concentrations

Station ID	Particulate (mg/m³)	Organic Vapor (ppm)	Mercury Vapor (µg/m³)
PM-1	0.012	0.00	0.01
PM-2	0.012	0.00	0.01
PM-3	0.012	0.01	0.01
PM-4	0.011	0.00	0.01
WZ-1	0.012	0.00	0.00
WZ-2	0.011	0.00	0.00
WZ-3	0.011	0.00	0.00
WZ-4	0.011	0.00	0.02

Maximum 15-Minute-Average Concentrations

Station ID	Particulate (mg/m³)	Organic Vapor (ppm)	Mercury Vapor (µg/m³)
PM-1	0.032	0.01	0.02
PM-2	0.029	0.00	0.02
PM-3	0.017	0.10	0.02
PM-4	0.014	0.01	0.03
WZ-1	0.015	0.00	0.01
WZ-2	0.015	0.00	0.01
WZ-3	0.014	0.09	0.00
WZ-4	0.013	0.00	0.05

•mg/m³ = milligrams per cubic meter •ppm = parts per million •µg/m³ = micrograms per cubic meter

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey,	Ву:	Jack Millman
	S. Simpson		LANGAN



Page 5 of 7

SITE OBSERVATION REPORT

Ambient Air (Handheld Jerome® J505 and Handheld PID)

- The dedicated mobile monitor (Langan) used a handheld Jerome® J505 mercury vapor analyzer to monitor ambient air conditions at various heights throughout the site. Instantaneous mercury vapor concentrations throughout the site ranged from 0.00 µg/m³ to 0.15 µg/m³.
- The dedicated mobile monitor (Langan) used a handheld PID to monitor VOC concentrations throughout the site. Instantaneous VOC concentrations were not detected above background concentrations throughout the workday.

Off-site CAMP Stations

- CAMP station WZ-1 was placed on the western sidewalk of Beekman Street from about 6:38am to 4:25pm.
- CAMP station WZ-2 was placed on the southern sidewalk of Water Street from about 6:40am to 4:30pm.
- CAMP station WZ-3 was placed on the eastern sidewalk of Peck Slip from about 6:42am to 4:37pm.
- CAMP station WZ-4 was placed on the northern sidewalk of Pearl Street from about 6:45am to 4:48pm.

Prior to CAMP Shutdown

Prior to discontinuing CAMP, mercury vapor and VOC concentrations were confirmed to return to background conditions at each perimeter station using the handheld Jerome® J505 mercury vapor analyzer and handheld PID, respectively. Perimeter CAMP stations were discontinued sequentially between 4:12pm and 4:18pm.

- Background concentrations of mercury vapor at each CAMP station were recorded at 0.00 μg/m³.
- Background concentrations of VOCs at each CAMP station were recorded at 0.0 ppm.

Anticipated Activities


- ECD will continue exporting C&D and soil/fill from the western part of the site for off-site disposal.
- ECD will continue installing soil mix columns and/or soldier piles for SOE installation along Pearl Street and Peck Slip.
- ECD will continue installation of timber lagging for the SOE system in the western part of the site.

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey,	Ву:	Jack Millman
	S. Simpson		LANGAN



Page 6 of 7

SITE OBSERVATION REPORT

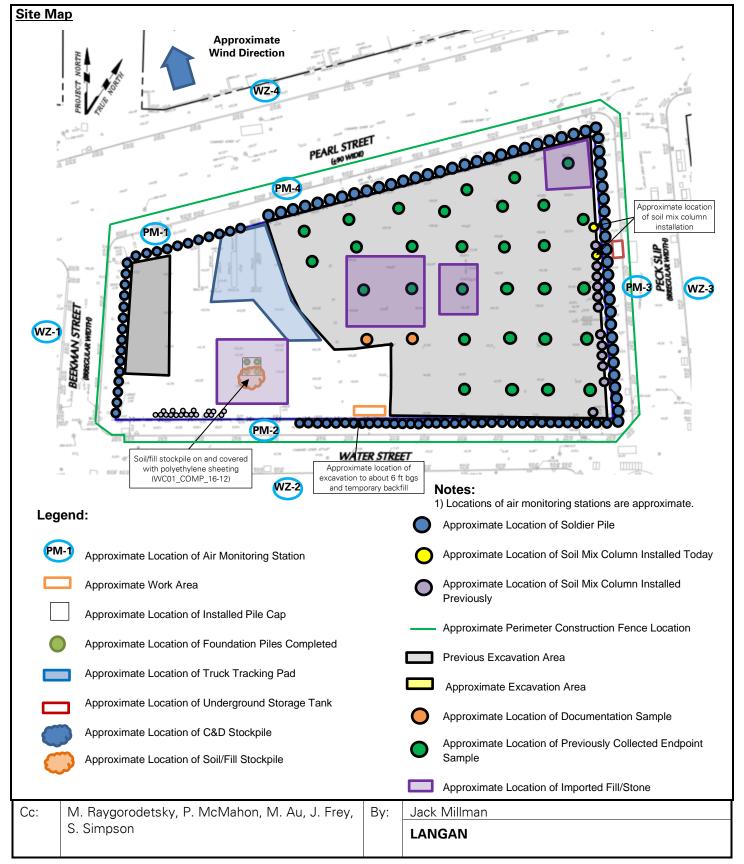



Page 7 of 7

SITE OBSERVATION REPORT

Select Site Photographs:



Photo 1: ECD installing a soil mix column in the eastern part of the site (facing north)



Photo 2: Atmos® AC-645 odor/vapor suppressing foam applied to soil/fill in the southern part of the site (facing northwest)

Cc:	M. Raygorodetsky, P. McMahon, M. Au, J. Frey,	Ву:	Jack Millman
	S. Simpson		LANGAN
