## INSPECTION REPORT

**Site Number:** V-00334-9/915525 Date: August 26, 2009

**Site Name:** Grief Bros. Corporation

**Location:** 2122 Colvin Blvd, Tonawanda

Project Manager: Michael J. Hinton

**Project Engineer:** Jon Fox ERM

**Job Phone:** N/A

**HEALTH & SAFETY:** PPE: Level D

Is the PPE level in conformance with the specifications: N/A Are atmospheric monitoring results at acceptable levels? N/A

## **DESCRIPTION OF WORK PERFORMED:**

MJH on site at 1120 hrs

Weather - overcast, rain, south west breeze, T~70°F ERM - Rob Sents, Todd \_\_\_\_\_ Marcor - 2 employees Nothnagel -2

Nothnagel coring and augering VP-2 well. Struggle to get skid mounted rig into pit. Some evidence of DNAPL flowed to surface when core was removed. Core completed at 1135 hrs

Air monitoring in place - all normal

VP-2 - PID at bottom of slab ~112, PID reading just above pit floor ~0. Soil sample from upper cuttings PID - ~1160. Soil sample from ~3' below pit floor PID ~1729. Soil sample from ~6' below pit floor PID ~2045 ppm. Visual evidence of DNAPL. Free product collects in bottom of bag. Evidence of DNAPL on floor from augers. VP-2 augers advanced to 6' below pit floor. 7' slotted PVC screen installed in VP-2 boring.

Pumped sump water and varnish from sump and floor drain. Pump caused strong varnish odor on factory floor.

Took photo's

MJH left site at 1340 hrs

**Attachments:** photo's

**Inspector's Name (Print):** Michael J. Hinton

Inspector's Signature: Date: August 31, 2009






082609-01 VP-2 Coring.JPG

082609-02 VP-2.JPG



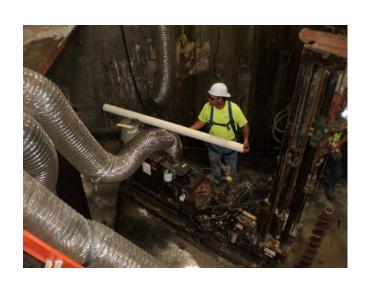

082609-03 VP-2 Augers.JPG Greif Bros

2609-04 VP-2 Typ slotted casing.J Page 1



082609-05 VP-2.JPG



082609-06 VP-2.JPG



082609-07 VP-2 Sand pack.JPG Greif Bros



082609-08 VP-2.JPG Page 2
