FOREST PRESERVE DETAILED PROJECT WORK PLAN

Fiscal Year 2023 Project # 2023-RB-21; CO-WP-325

Region Five		Project Title	_				
Five		Upper Saranac Lake Lean-to installation					
Project Type	Town(s)	County	Management Unit				
New Construction	Harrieststown	<u>Franklin</u>	Saranac Lakes Wild Forest				

Description of Desired Condition(s) for Project

The desired conditions for this project are based on the desired conditions statement in the Saranac Lakes Wild Forest Unit Management Plan for primitive tent sites. The desired conditions are to provide and maintain well-designed and constructed facilities for public use that promote resource protection and will maximize long term sustainability. Choosing a suitable location ensures initial and long-term environmental protection. These facilities will include a usable fire pit and a sanitary privy. Beyond the obvious environmental benefits, these facilities add to the user's experience as much as a desirable location does. Desired conditions for the project site will be minimal expansion from the designed footprint of the built facility, no negative impacts on adjacent vegetation, minimal signs of compaction, no occurrences of human waste or litter, and providing an enjoyable user experience. Since this lean-to will be installed at an existing primitive tent site that has a large, impacted area, it is further desired that the lean-to will result in use being concentrated to a smaller area due to the prevention of tent sprawl outward from the site. This could increase the chances for successful site restoration work.

Description of Project Specifications

This project will install a new lean-to at existing primitive tent site number 17 on Upper Saranac Lake. The current primitive tent site receives significant levels of use, and the impacts from the use are spread over a large area. The lean-to will be installed more than 100 feet from the lake shore. The lean-to for this project will follow the standard Adirondack lean-to design. The Saranac Lakes Wild Forest Unit Management Plan allows for five lean-tos to be built at primitive tent sites in the unit. This will be the first lean-to built under this provision.

<u>Description of Measures Taken to Avoid, Mitigate and Minimize Impacts to Natural Resources</u>
<u>Trees to be removed</u>: The lean-to will be located to minimize the number of trees that will need to be removed. Five trees over three inches in diameter at breast height (DBH) will need to be removed for this project.

<u>Earthwork and disturbance</u>: Earthwork for this project will be limited to the need to move and set foundation rocks at each of the lean-to's corners.

<u>Impacts to streams, waterbodies, and wetlands</u>: This project is located more than 100 feet from any stream, waterbody, or wetland; including Upper Saranac Lake. The minimal amount of earthwork and tree cutting proposed will not impact these resources.

Rare, threatened, or endangered species: There are no rare, threatened, or endangered species documented within 0.25-mile of the project site.

Analysis of Project Location and Design Alternatives

The primary alternative for this project would be to not install the lean-to. The installation of the lean-to will provide a more enjoyable user experience and concentrate environmental impacts where they can be mitigated through siting and design. This will allow for a decrease in overall impacted area. Not installing the lean-to would result in no change to the current situation.

Description of Use of Motorized Equipment and/or Motor Vehicles (if any)

Motorboats will be used to transport the materials to the site. Power tools may be used for the assembly of the lean-to. All proposed motorized use is allowable in this area.

Description of Applicable Standards for Accessibility by People with Disabilities

The primitive tent site where the lean-to will be installed does not meet accessibility standards. Since this proposal does not suggest changes to the overall site design to comply with accessibility standards, this lean-to will be built following the standard Adirondack lean-to design.

Other Relevant Considerations

Prepared by (Name & Title): Steve Guglielmi Date: 7/31/2023

Phone: 518-897-1286

REGULATORY CLE	YES NO (NAME) rces Restricted Burning										
PROGRAM	PERMIT				COMMENTS						
				(NAME)							
Air Resources	Restricted Burning		\boxtimes								
Mineral Resources	Mining		\boxtimes								
Materials Management	Solid Waste Mgt. Fac.		\boxtimes								
	Dam Safety Review		\boxtimes								
Water Spills Management Lands and Forests Fish and Wildlife Compliance Services	Const. in Flood Hazard		\boxtimes								
	Public Water Supply		\boxtimes								
	SPDES		\boxtimes								
Spills Management	Petro. Bulk Storage		\boxtimes								
Air Resources Mineral Resources Materials Management Water Spills Management Lands and Forests Fish and Wildlife	Unit Management Plan	\boxtimes		Steve Guglielmi	adopted in 2019						
	Tree Cutting	\boxtimes		Steve Guglielmi	part of application						
	Protected Native Plants		\boxtimes								
	Historic Preservation		\boxtimes								
Fish and Wildlife	Freshwater Wetlands		\boxtimes								
	Wild Scenic & Rec. River		\boxtimes								
	Other Protection of Waters		\boxtimes								
	EAF		\boxtimes								
Compliance Services	Negative Declaration		\boxtimes								
	Env. Impact Statement		\boxtimes								
	Water Quality Cert.		\boxtimes								
	CP-17		\boxtimes								
Mineral Resources Materials Management Water Spills Management Lands and Forests Fish and Wildlife Compliance Services DEC (other)	Commissioner (aircraft,motorized equipment)		\boxtimes								
	Flight Request		\boxtimes								
	Contract Clearance Sh.		\boxtimes								
	DOB Exemption		\boxtimes								
	APA MOU		\boxtimes								
Other Agencies	APA Wetlands Permit		\boxtimes								
	Corps. of Engineers		\boxtimes								
	Building Permits		\boxtimes								
	Local Permits		\boxtimes								
	Easements		\boxtimes								
	Highway Enter DOT		\boxtimes								
	Wastewater Disposal		\boxtimes								

State Land Tree Tally


Project: Installing a Lean-to on Upper Saranac Lake

State Land Unit: Saranac Lakes Wild Forest

County: Franklin Town: Harrietstow

Date Tallied: 5/17/2023 Tallied By: Steven Guglielmi

Species		Diameter Class (inches)								Total					
	2	4	6	8	10	12	14	16	18	20	22	24	26	28	
birch, paper						1									1
hemlock			2	2											4
Total	ا م	٥	۱ ء	2		1	۱ ۵	۱ ۵	۱ ۵	۱ ۵	۱ ۵	۱ ۵	۱ ۵	ا م ا	_
Total	0	0	2	2	0	1	0	0	0	0	0	0	0	0	

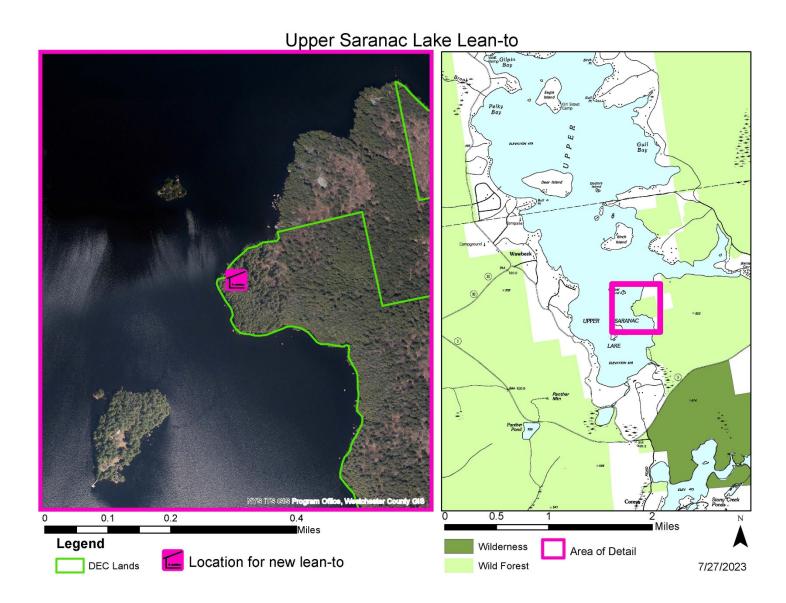



SARANAC LAKES WILD FOREST

and

Lake Placid Boat Launch
Lake Flower Boat Launch
Upper Saranac Lake Boat Launch
Raquette River Boat Launches

Unit Management Plan

River Area Management Plans

Saranac River, Ausable River, and Raquette River

Final Environmental Impact Statement

NYS DEC, REGION 5, DIVISION OF LANDS AND FORESTS

P.O. Box 296, 1115 State Route 86, Ray Brook, NY 12997-0296 r5.ump@dec.ny.gov

www.dec.ny.gov April 2019

Detailed Work Plan Rev. 04/28/2023 to accessibility standards may exceed the minimum standards. Accessible primitive tent sites will not be designated as reserved for exclusive use by persons with disabilities, but information may be posted at the sites informing users that it has been built to accessibility standards and to encourage that persons with disabilities be accommodated at the site.

- A reduction in the number of primitive tent sites on some ponds could greatly increase the demand for the remaining sites. To increase site availability, the length of time that a party can camp on a pond may be limited to one week. Initially this will apply to Follensby Clear Pond and Polliwog Pond. This restriction may be ended or expanded to additional areas as deemed necessary. This restriction may be rescinded during the big game hunting season, so that the long-term camping permits could still be issued for duration of the big game hunting season.
- To accommodate a variety of campers, some tent sites may be reserved for campers not needing a length of stay permit.
- All new or relocated primitive tent sites will comply with APSLMP requirements.
- The lean-to on Follensby Clear Pond is too close to the water and the island it is on is not large enough to allow a privy to be built with the required set back distance. This lean-to will be removed, and camping will not be allowed at this site (see map 2).
- When the lean-tos on Lake Placid need major repair work they will be moved farther from the water but will remain at the same general location.
- Five new lean-tos may be built at designated primitive tent sites in the unit. New lean-tos will be set back 100 feet from the mean high-water mark of lakes, ponds. rivers, or major streams. New lean-tos will not be built at roadside campsites or on islands that are less than 15 acres in size.
- Primitive tent sites will be numbered where there are more than two sites along the same feature (such as road, pond, or river). This numbering will extend to adjacent units when necessary, for example the Raquette River, Moose Pond, and Coreys Road.
- The campsite closures will occur as the new sites are built.

6

- All temporarily or permanently closed primitive tent sites will be restored toward a natural condition. Fire rings and other evidence of past use will be removed. Erosion will be controlled and vegetation (nursery stock or transplanting of native plants) will be planted.
- At fire sensitive areas, the Department has the discretion to place sand, a cement slab, or similar material under fire rings.

Saranac Lakes Wild Forest – Unit Management Plan – April 2019 149

> Detailed Work Plan Rev. 04/28/2023
