


CONSTRUCTION SKETCH

PROJECT Bethpage, NY GM-38 Area
 JOB NO. CTO 96
 DRILLING SUBCONTRACTOR Uni-Tech Drilling
 DRILLER Karl Hitzelberger

DRILLING METHOD Reverse Rotary
 WELL NO. RW-1
 DATE OF WELL INSTALLATION April 4-7, 2005
 GEOLOGIST Vince Richards
 TOP OF CASING ELEVATION 87.70' ASL

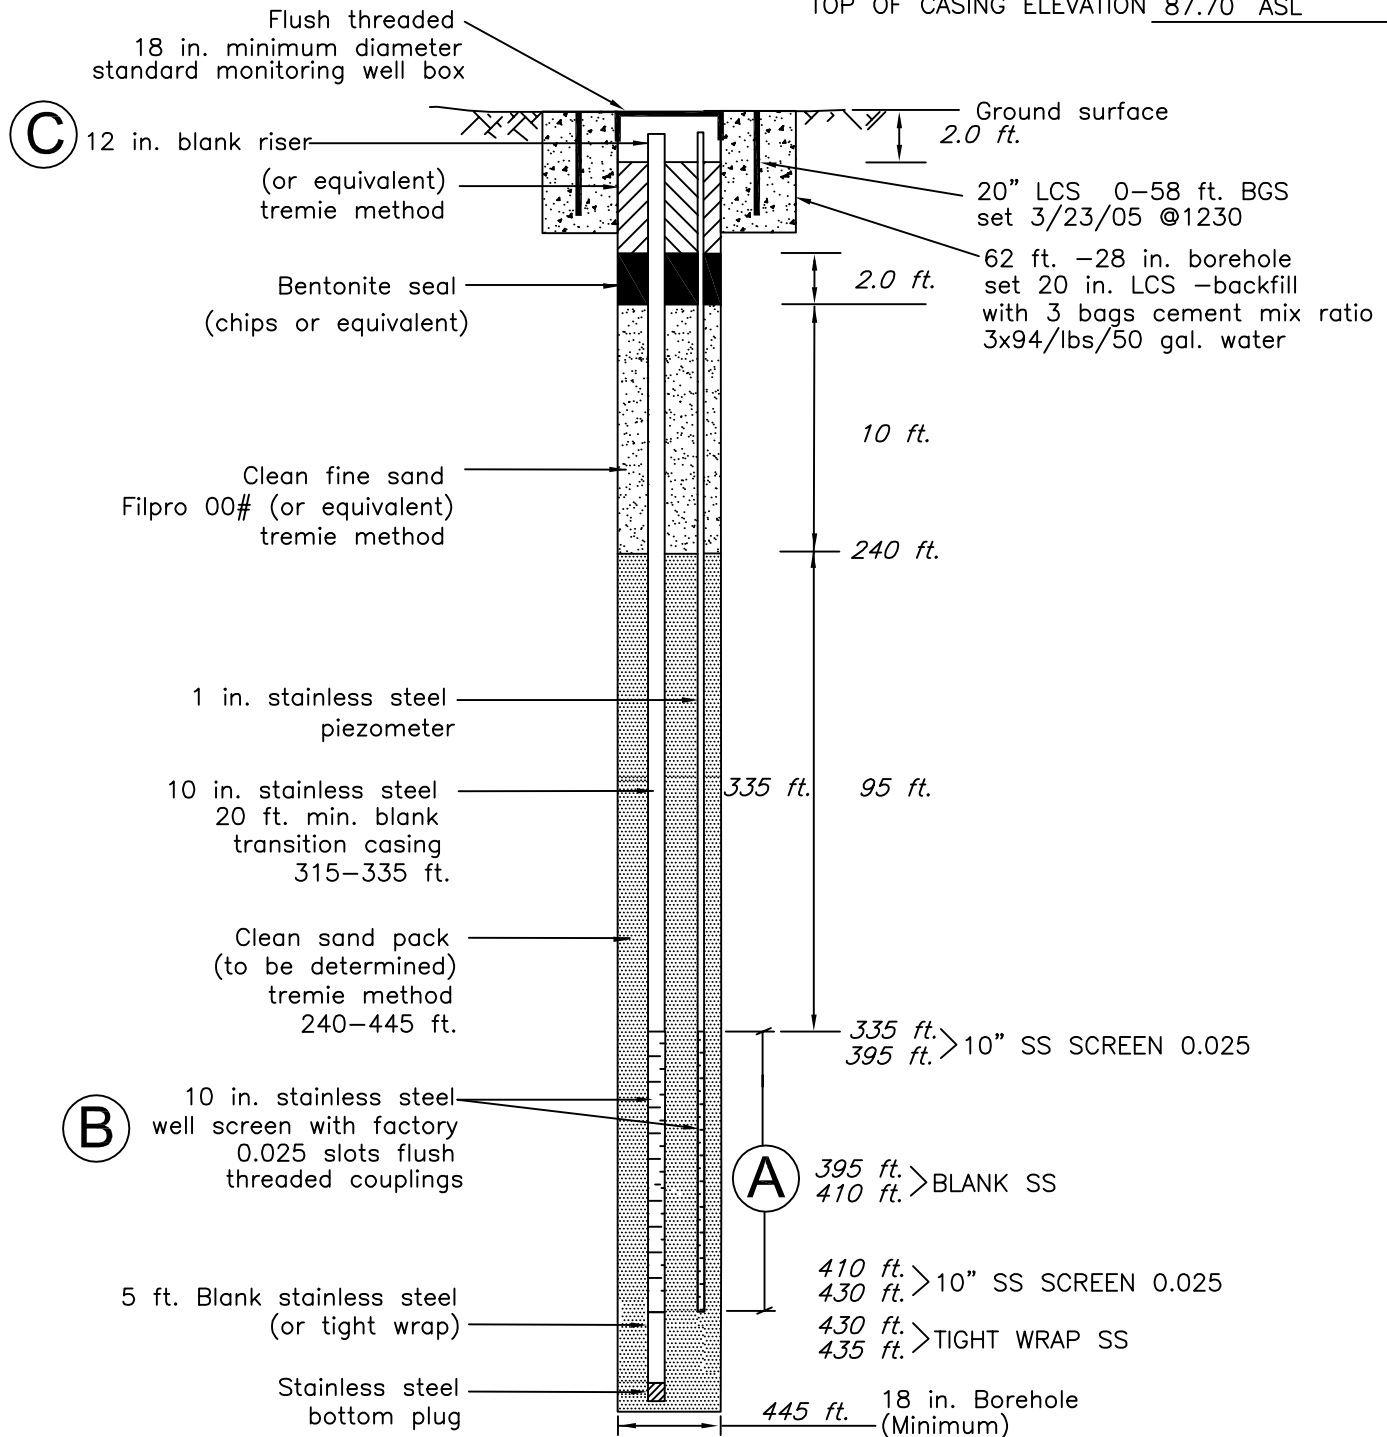


	(A)	(B)	(C)
WELL ID	SCREEN INTERVAL (FT. BGS)	SCREEN MATERIAL	CASING MATERIAL
RW-1	335-395 410-430	304 SS FT-WIRE WRAPPED	WELDED CS

SS = STAINLESS STEEL
 CS = CARBON STEEL (SCH 40)
 FT = FLUSH THREADED

U.S. Navy RAC
 Engineering Field Activity-Northeast
 NWIRP, Bethpage, NY
 GM-38 Area
 Groundwater Remediation Project

Recovery Well No. 1 Construction Diagram

 **TETRA TECH EC, INC.**
